

Vegetation Clearing & Fauna Management Plan

*Economic Development
Queensland (EDQ) / Bundaberg
Regional Council (BRC)*

Bundaberg Hospital




CONTENTS

- 11612 E 02 VCFMP A** -- Vegetation Clearing Notes
- 11612 E 03-04 VCFMP A** -- Fauna Notes
- 11612 E 05 VCFMP A** -- Detail Sheet Context
- 11612 E 06 - 17 VCFMP A** -- Detail Sheets
- 11612 E 18 VCFMP A** -- Clearing Direction
- Appendix A** -- RPS Tree Schedule

SHG Contact

Ms Madeline Dooley
Email: mail@saundershavill.com

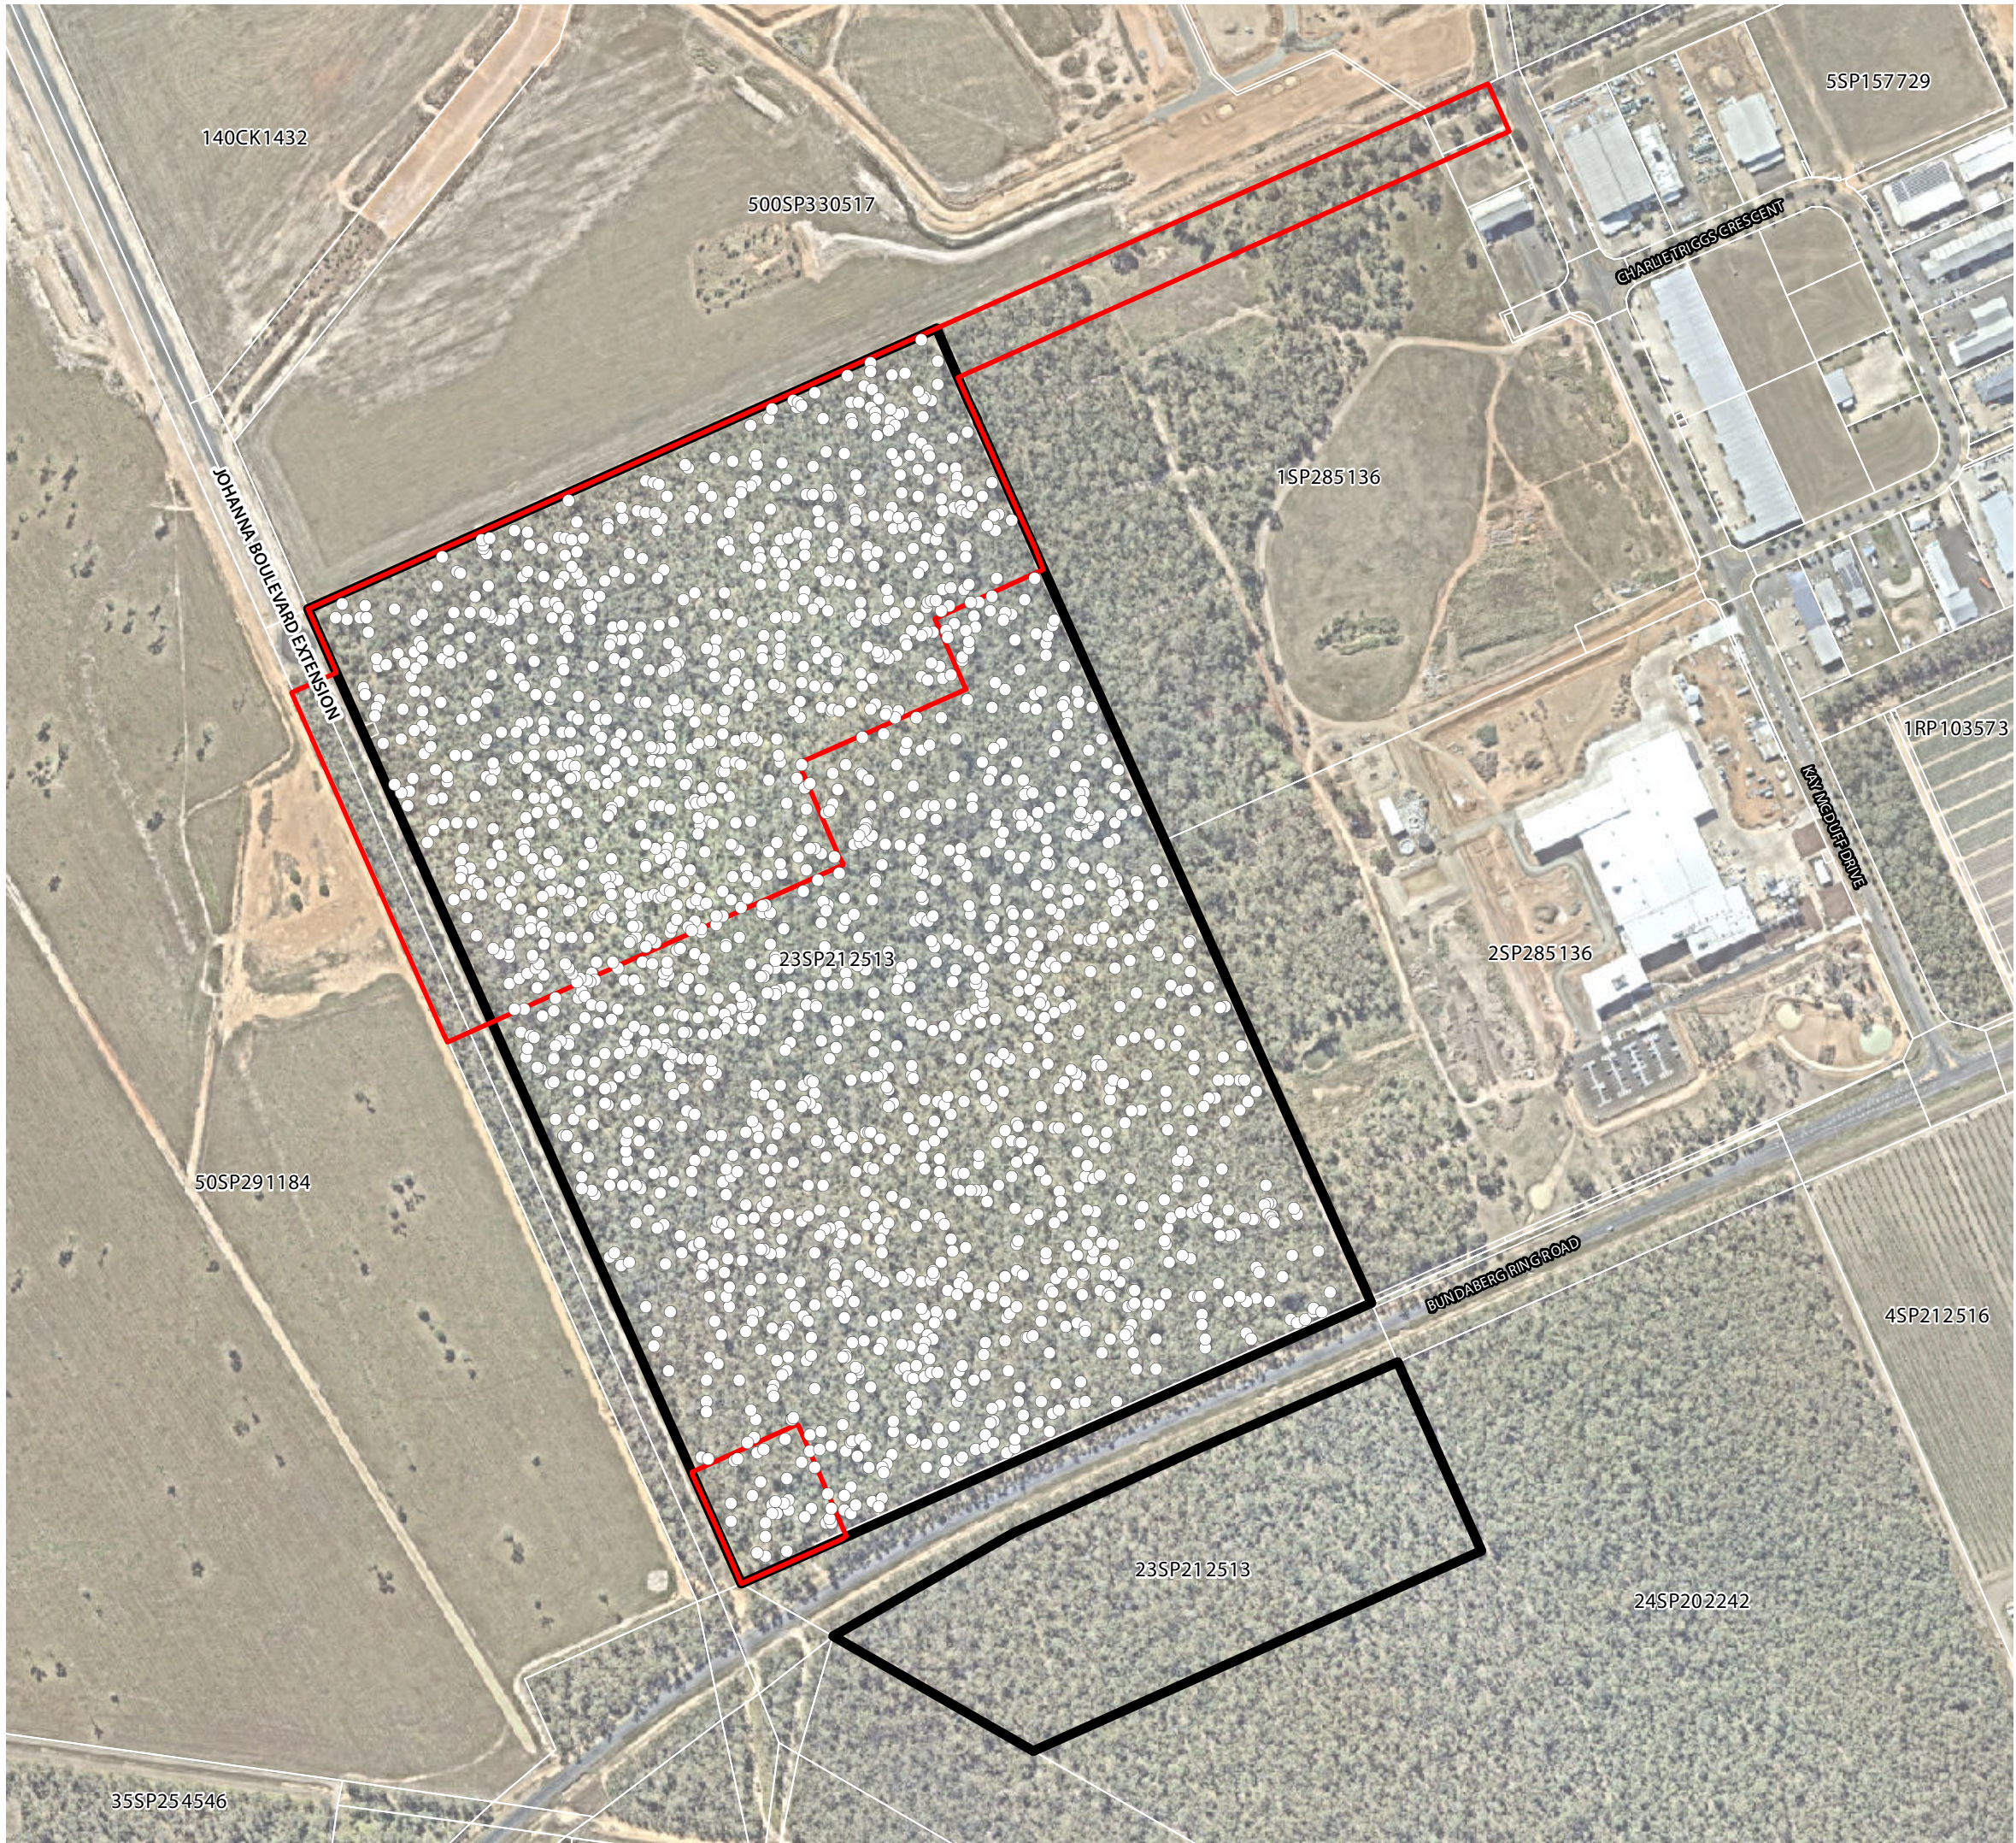

Vegetation Clearing and Fauna Management Plan - Notes

Introduction

The Environmental Management Division of the **Saunders Havill Group (SHG)** was engaged by **Queensland Health** to prepare a Vegetation Clearing and Fauna Management Plan (VCFMP) for the proposed Bundaberg Hospital site at Lot 23 Bundaberg Ring Road, Thabeban, QLD, 4670 (Lot 23 on SP212513).

The purpose of this plan is to manage the vegetation removal process and the protection of fauna species within the disturbance area. This VCFMP has been prepared for Bundaberg Regional Council (BRC)/Economic Development Queensland (EDQ) and is required to be approved prior to clearing works commencing. The clearing works will follow general principles for vegetation clearing documented on this sheet and *Sheet 3*, and all Council/EDQ specific requirements.

This VCFMP has been produced by overlaying the following site datasets to determine impacts and disturbance on existing vegetation:

1. Tree data including specimen details & features (RPS, 2023)
2. Site Inspection of Existing Vegetation (RPS, 2023)
3. Site Layout Plans (Stantec, 2023)
4. Arborist inspection (TBD)

Project Management

Vegetation management and processes are an integral part of the construction and operational works phases. The site supervisor is responsible for all onsite works including overseeing vegetation clearing, health and safety of fauna and adhering to Council's / EDQ's conditions and guidelines and Australian Standards - Protection of Trees on Development Sites AS4970-2009 and Pruning of Amenity Trees AS4373-1996.

When required, the project arborist (with minimum AQF Level 5 in Arboriculture and minimum 5 years' experience) is responsible for: undertaking all appropriate arboricultural measures prior to the commencement of any earthworks on site to ensure the survival and long-term health of existing trees to be retained. These measures may include soil decompaction, soil aeration, fertilising, mulching, watering, root or crown reduction and hazard reduction or as otherwise determined by the arborist. The site arborist is also required to direct and supervise all works within TPZs of trees to be retained, and perform arboricultural care requirements where necessary.

The roles and responsibilities of the Fauna Spotter-catcher are provided on *Sheet 3*.

Site Contacts

Site and consulting contacts for queries relating to vegetation clearing include:

Client Contact: Queensland Health	Environmental Contact: Saunders Havill Group E: mail@saundershavill.com
Site Contractor: <i>To be advised</i>	Site Arborist: <i>To be advised</i>
Site Fauna spotter-catcher: <i>To be advised</i> (Refer to <i>Sheet 3</i> for responsibilities)	Site Bushfire Consultant: <i>To be advised</i>

Clearing Phases and Process

PHASE 1 - Tree Protection Fencing to be installed

Fencing to be installed prior to the commencement of any clearing works on the site. Tree protection fencing to be located at or beyond 12 x diameter at breast height (DBH) (AS4970-2009 Protection of trees on development sites)—unless approved by the appointed arborist. Signs identifying the tree retention area as a 'no go zone' to be installed at regular intervals along tree protection fencing.

PHASE 2 - Council Pre-start Meeting (if required by Council/EDQ)

Fencing shall be in place at the time of the official pre-start meeting for inspection and sign off by Council/EDQ Officers.

PHASE 3 - Fauna Inspections and Management

Undertake necessary fauna management requirements prior to clearing works - as a minimum, this should include the specifications listed on *Sheet 3*, and acknowledge specific Council/EDQ approval requirements.

PHASE 4 - Undertake Bulk Clearing

Undertake wholesale removal of vegetation once approved for removal by a qualified fauna spotter and all necessary permits are obtained. Clearing will occur in the direction outlined in *Sheet 5* of this VCFMP, and managed by the appointed fauna spotter-catcher to allow all fauna to move unimpeded towards retained vegetation on, and adjacent to, the site.

Vegetation clearing techniques:

- i. By utilising the most appropriate machinery and equipment during vegetation clearing, the probability of injury or death of wildlife during clearing can be significantly reduced or eliminated while still maintaining an efficient vegetation removal process.
- ii. Suggested techniques are as follows: (a) a vertical tree grab attachment on an excavator (30 tonne) can be used to pull entire trees in size up to 30-40cm diameter at a height measured at 1.3 metres above ground level and lay them down in a steady controlled fashion, allowing inspection by a fauna spotter-catcher (b) where large trees are too large for a vertical tree grab and have been identified, an elevated work platform or where practical, cherry picker should be used in conjunction with a chainsaw operator and fauna spotter-catcher. Alternatively, careful removal of hollow section from habitat tree and gentle lowering for inspection by fauna spotter-catcher (c) the use of bulldozers to clear vegetation is limited to vegetation that has been thoroughly inspected by a fauna spotter-catcher and is found to contain no fauna or potential habitat. Bulldozers are not to be used to push over large trees that contain hollows or other habitat features.

NOTE: Dogs are not permitted onsite at any time during construction. Construction works including clearing must occur between the hours of 6.00am and 6.00pm.

Access and Stockpiling


Vegetation stockpiling locations are to be designated in easily accessible areas outside of TPZs. Indicative vegetation stockpiling locations have been allocated within the clearing area, allowing for material to be easily delivered and stored. These locations are subject to minor change according to cut/fill activities and intended location for reuse.

Cleared vegetation free of weeds is to be reused on or off the project site. Recycling techniques include mulching, tub-grinding, wood chipping and salvage (e.g. custom milling). Trees with identified hollows should have the hollow section preserved and should be suitably mounted on nearby or adjacent suitable trees.


Maintenance

After tree clearing works on site, an analysis of the vegetation's health and growth should be undertaken by the project arborist to determine specific maintenance needs. Follow-up maintenance works should be carried out on retained vegetation where required. If conditioned in the approval—the project arborist may be required to submit a report to Council/EDQ detailing the measures undertaken during the construction period and any further work required post this period.

Tree Protection Zone - Detail (not to scale)

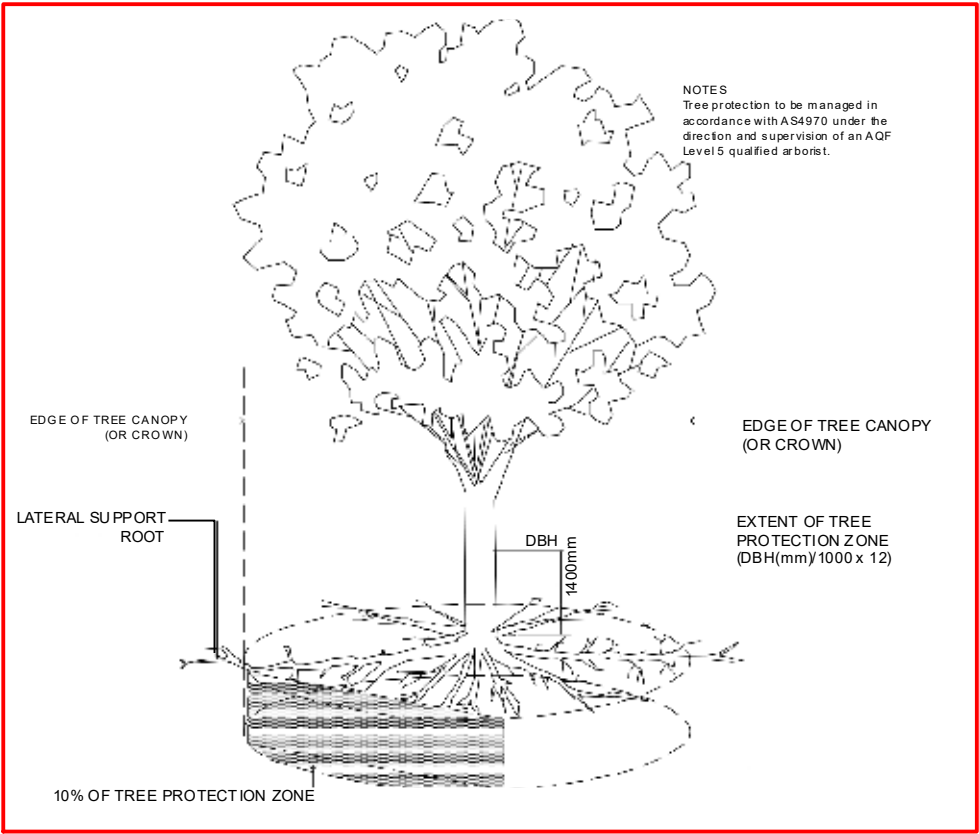

Tree Protection Fencing - Detail (not to scale)

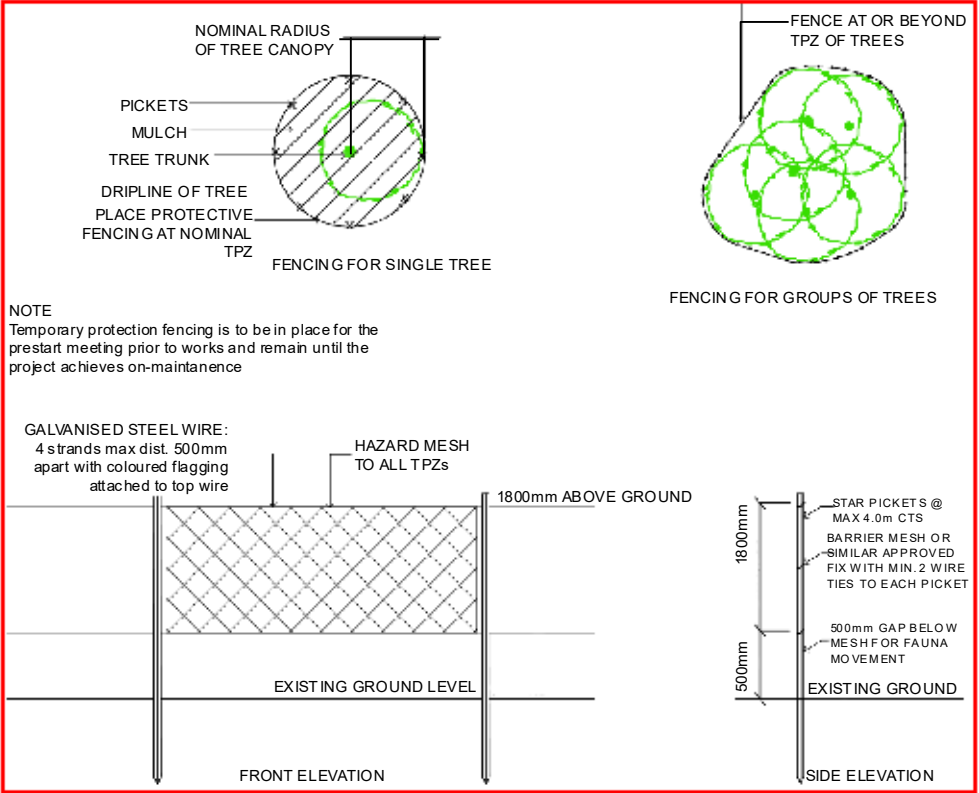

Bundaberg Ring Road, Thabeban

Vegetation Clearing and Fauna Management Plan - Notes

Introduction

The Fauna Management specification on this *VCFMP* is designed to protect native animals and control/manage impacts during the vegetation clearing works. The clearing area occurs within the northern and south-western sections of the site. The site abuts cleared land and active construction zones to the north and west, Bundaberg Ring Road to the south, and a brewery and other industrial land uses to the west. Common species associated with semi-urban landscapes were spotted at the clearing area during the field assessment. The fauna management specifications and principles incorporated in this *VCFMP* apply generically to all native animals and focus on avoiding conflicts and incorporating measures to minimise disturbance. Compliance with this section of the *VCFMP* is compulsory and incorporates the use of expert consultants including a Fauna Spotter (holding a valid Wildlife Rehabilitation Permit issued by the **Department of Environment and Science**). The management protocols outlined in the following section can vary at the site, as determined by the registered fauna spotter catcher or arborist.

Fauna Impacts

Clearing of vegetation provides an obvious source of impact to existing habitat and animal safety. More specifically the existing vegetation provides habitat, movement and protection opportunities for some fauna through both regrowth and canopy trees. These opportunities may be altered during and post vegetation clearing works. Potential impacts include:

Construction Impacts

- Direct removal of site vegetation
- Loss of habitat
- Noise, vibration and dust
- Erosion and sedimentation
- Threats associated with open cuts etc. and fauna entrapment
- Loss of food sources
- Excavation/compaction/changes in ground levels
- Altering hydrological flows
- Fragmentation of habitat

Operational Impacts

- Weed introduction (garden escapees)
- Increased hydrology with increased hardstand
- Altering of run-off chemical and nutrient components (quality)
- Barriers to fauna movement
- Vehicles and pedestrian movement and trespass
- Introduction of domestic and predatory species


Fauna Management Schedule

1.0 Pre - Clearing				
Ref:	Management Item	Responsibility	Timing	Reporting
1.1	Temporary Fencing Prior to the commencement of works and to be inspected by the site Environmental Coordinator and/or Project Arborist—Delineate areas where vegetation is proposed to be retained with exclusion fencing to prevent accidental felling. Clearing is to be undertaken in accordance with AS 4970-2009 Protection of Trees on Development Sites. ▪ Fencing shall be fauna friendly ▪ No clearing, stockpiling, site access, earthworks, storage, etc. is to occur within the temporary protection fencing. ▪ Only approved weed management works to occur within the temporary protection fencing ▪ Fencing to be reinstated immediately if damaged or knocked down, any damage to retained trees to be immediately reported to Project Arborist. ▪ Fencing to remain until the completion of all site works.	Site Supervisor	Prior to the commencement of clearing	Inspected by Council / EDQ and Project Arborist
1.2	Contractor Education & Awareness All site contractors and subcontractors will be made aware of their responsibilities to protect native fauna. The Fauna Management notes on this VCFMP are provided as a working document to assist on-site management and protection of native animals. This generally will form part of education and training on a broader work place health and safety but as a minimum will include: ▪ Copy of VCFMP kept on-site (Site Office). ▪ General education and awareness notification of contractors and sub-contractors involved in activities potentially impacting native animals as part of site induction – contractors must know the location of the VCFMP, key phone numbers and who to report to if they breach the VCFMP. ▪ A list of relevant contact phone numbers as listed on these drawings is kept in a visible and accessible location in the site office.	Site Supervisor / The Proponent	Prior to the commencement of clearing and as part of the site induction for new staff and sub-contractors	Site Supervisor
1.3	Fauna Spotter-Catcher / Relocator Immediately prior to the commencement of clearing of native vegetation, a daily visual inspection of the area must be carried out by a qualified fauna spotter-catcher holding a valid Rehabilitation Permit from the relevant State Government Agency. The fauna spotter-catcher should clearly flag vegetation found to contain fauna or fauna habitat (such as tree hollows, arboreal termite mounds, stick nests or possum drays with flagging tape and verbally communicate this information to the tree feller to ensure flagged trees are not felled until authorised by the fauna manager.	Site Supervisor	Prior to the commencement, of clearing	Inspected by the Fauna Spotter-catcher
2.0 Vegetation Clearing				
2.1	Fauna Spotter-Catcher / Relocator The qualified fauna spotter-catcher is to be present on site during all clearing operations to supervise and direct clearing works, and to respond to any situations that may arise in relation to fauna. In the event of an animal being located, a suitable buffer area (as determined by the fauna spotter-catcher) should be established around the animal’s location that excludes machinery until it has relocated at its own accord (usually overnight). If an animal requires relocating this must be undertaken by a suitable qualified fauna expert recognized by the Department of Environment & Science . For some fauna, specific permit requirements may apply. If vegetation is left stockpiled for more than 12 hours or overnight, the fauna spotter-catcher must inspect the vegetation prior to chipping or removal from site. The Fauna Spotter-catcher will manage the care of any injured or orphaned wildlife (e.g. veterinary attention or delivery to a wildlife carer). Any native fauna listed as a threatened species under the Nature Conservation Regulation 2020 that are injured or orphaned by the development process, must be reported to the Department of Environment & Science (1300 130 372). Any other injured or orphaned fauna must be reported through the Rehabilitation Permit return process by the Fauna Spotter-catcher. The Site Supervisor is responsible for the safe management of site fauna and implementation of these specific fauna requirements.	Site Supervisor	During / post clearing	Inspected by the Fauna Spotter-catcher
2.2	Specific Koala Management Notes A Koala/Fauna spotter-catcher is a person who holds a valid Rehabilitation Permit from the relevant State Government Agency, and has either a tertiary qualification in Biology or Zoology, or who is demonstrably experienced in the identification and location of Koalas in their natural habitat. For example, a koala keeper employed by a licensed Wildlife exhibitor (i.e. a zoo) may be capable of demonstrating competence in locating Koala’s. Prior to the commencement and during felling operations, it is the responsibility of the Koala spotter to be present at the site of felling operations identify any tree at the site within which a Koala is present, as well as any tree that has a crown which is intermeshed or overlapping with such a tree; and advise the person who is authorised to conduct the felling operation, or that persons’ representative, of the precise location of each such tree Management Item.	Site Supervisor	Prior to the commencement, and during clearing	Inspected by the Fauna Spotter-catcher

Bundaberg Ring Road, Thabeban

Vegetation Clearing and Fauna Management Plan - Notes cont.

2.0 Vegetation Clearing (cont.)				
2.3	Clearing Pattern / Fauna Flushing Clearing occurs once the fauna spotter-catcher gives sign off the site is clear of all native species and all necessary permits are obtained. The intended clearing direction is towards retained vegetation. Clearing direction is subject to amendment by the fauna spotter-catcher. At the completion of operational works, and prior to the sealing of survey plans for the relevant stage, the fauna spotter-catcher must provide certification to Council / EDQ officers that all works were undertaken in accordance with these fauna management requirements and specific Council/EDQ requirements.	Site Supervisor	Prior to the commencement, and during clearing	Inspected by the Fauna Spotter-catcher
2.4	Specific Habitat Tree Notes Where possible, clearing of habitat trees is to be avoided during late winter and spring (typically July – October) when many native birds are actively nesting/have young in nests and arboreal mammals have dependent and/or pouch young.	Site Supervisor	Prior to the commencement, and during clearing	Inspected by the Fauna Spotter-catcher
2.5	Hollow / Habitat Feature Salvage Notes Hollows and other habitat features such as large fallen logs, log piles, rock piles or outcrops may provide important refuges / protection for fauna within bushland and open space areas near the development site. There are currently no regulatory guidelines in Queensland for the salvage and reinstallation of hollows and habitat features at development sites. The information below has been extracted from nest box installation material provided by MBRC, Redland and Ipswich City Council, and "Nest boxes for wildlife, a practical guide" by Alan and Stacey Franks (2015). The salvage and reinstallation of hollows and habitat features is to be undertaken by / or under the supervision and direction of a suitably qualified fauna spotter-catcher or arborist, and in accordance with these guidelines. The reinstallation of hollows and habitat features is required to comply with the bushfire management requirements of the receiving area. Salvage from clearing area: - Hollows should only be salvaged in circumstances where clearing of habitat trees cannot be avoided. - Habitat or hollow-bearing trees are to be felled last and cleared using special plant and equipment aimed at reducing the risk of death or injury to occupying fauna - Donor habitat tree particulars to be documented by the suitably qualified fauna spotter-catcher or arborist prior to salvage—including but not limited to tree species, height and diameter at breast height (DBH), height above ground and aspect of hollow, any other significant features. - Hollow / habitat feature sections from each identified habitat tree to be carefully removed by, or under direction and supervision of a suitably qualified fauna spotter-catcher or arborist. All additional trees to be inspected on ground to ensure all habitat features are salvaged from the clearing area. - Additional habitat features, such as site logs and rock should be inspected by the fauna spotter-catcher prior to relocation. Reinstallation at receiving area: - Hollows are to be salvaged and reinstalled at a suitable receiving area within an environmental area onsite, or as close to the site as possible. - The salvaged hollow is to be reinstalled in a similar tree specimen, and at a similar height and aspect as the donor tree where it is practical and safe to do so. - As a general rule, salvaged hollows should be positioned: - in a tree species preferred by the target fauna species. For example, Phascogales prefer rough-barked trees whereas Scaly-breasted Lorikeets prefer smooth-barked or dead trees - at a location in the receiving tree to meet the target species requirements - high enough in the receiving tree to reduce the chances of predation by introduced fauna species, and out of reach of humans. Greater than 4 metres (12 feet) above ground level is recommended to minimise predation from cats - away from potential edge effects to further mitigate feral uptake - where they can be easily inspected/maintained - away from bright lights - in a direction that is protected from severe storms and / or prevailing winds. A north-east to south-east aspect is preferred by many species - in a location that is shaded during the hottest parts of the day. - Where they are least vulnerable to branch fall - level with a tree branch to provide easy access for fauna - firmly mounted with least impact to the tree - If not practical or safe to install a tree hollow / habitat feature in a tree at the receiving area, it should be positioned on ground providing there are no conflicts with bushfire requirements at the receiving area. Other habitat features may be strategically positioned at the receiving area to optimise habitat and movement opportunities for fauna. Where possible, rocks and log material should be piled to increase habitat values.	Site Supervisor	Prior to the commencement/ and during clearing	Fauna spotter-catcher or arborist

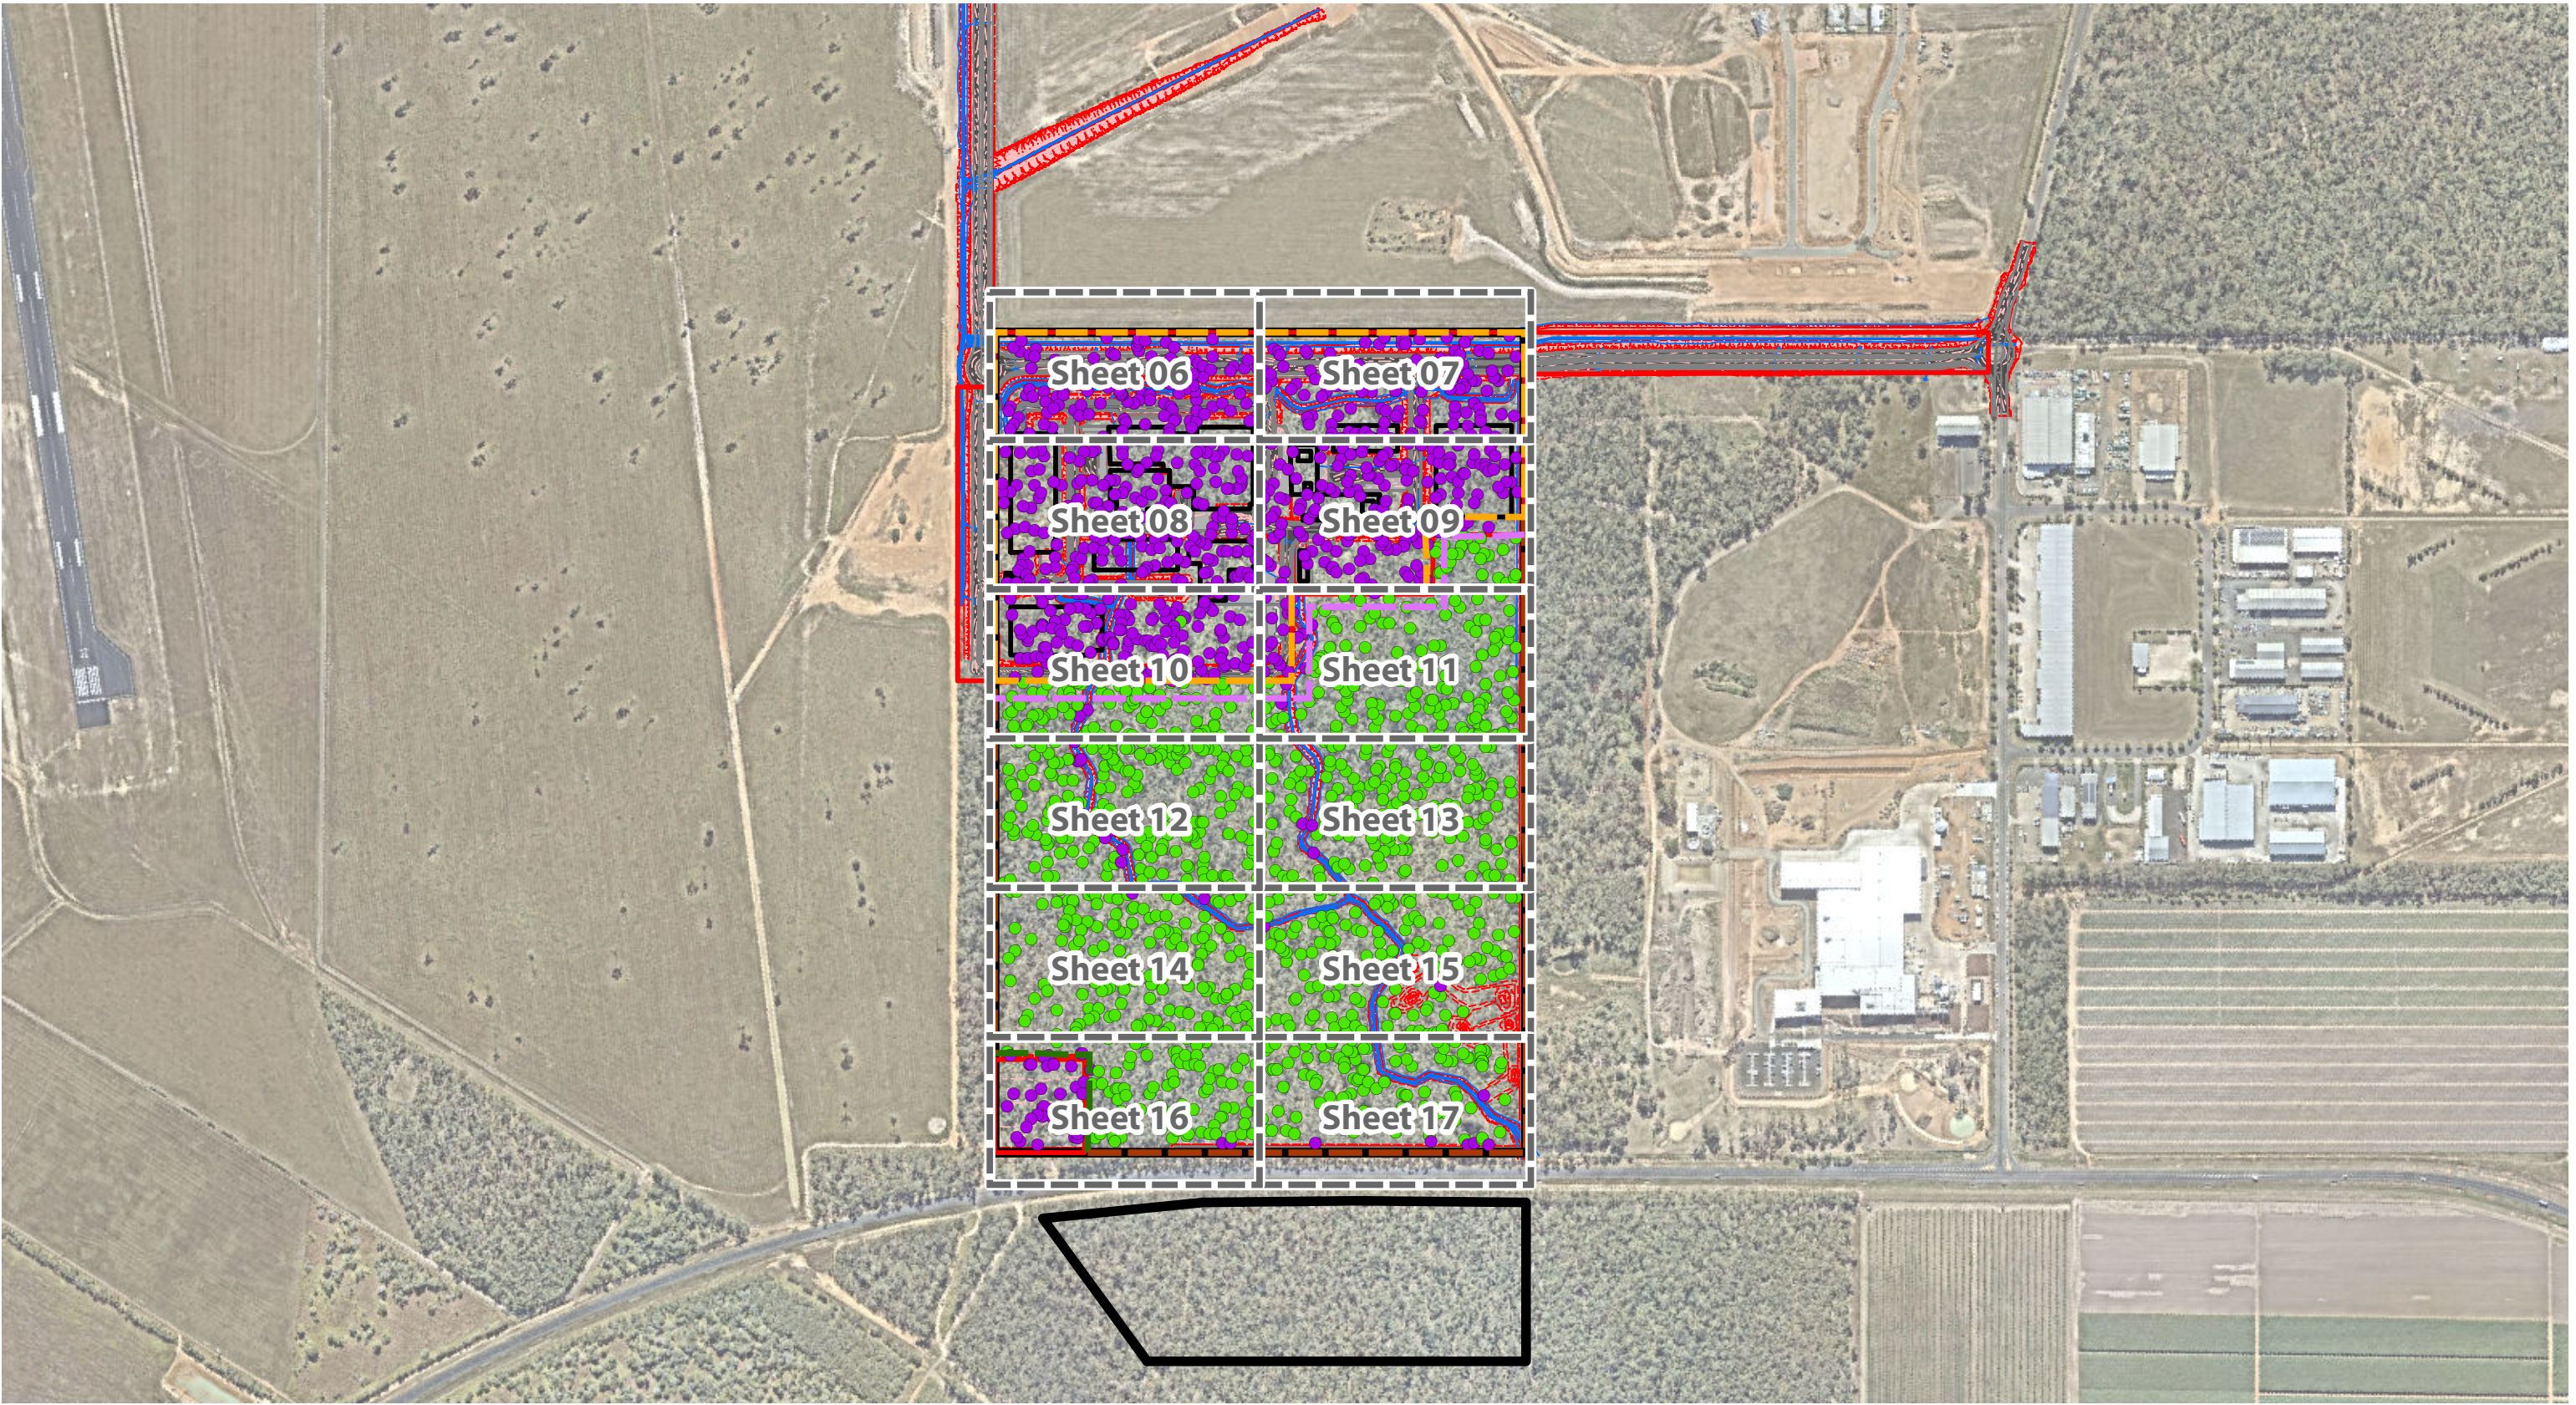

RPS Tree Plot

- Tree to retain
- Tree to retain subject to detailed stormwater design
- Tree to remove

Engineering Detail

- ▭ Disturbance Area
- ▭ Proposed Buildings
- ▭ Proposed Roads
- ▭ Proposed Footpaths

— Road and Footpath Detail

— Stage Boundaries

▭ Retaining Walls

— Stormwater Design


--- Earthworks Batters

--- Design Contours

Fencing Locations (External, Indicative)

- 1500h Boundary Fencing - dimbale/fauna-friendly wire fence (replace existing dilapidated log fence)
- 1800h Fence (Energy QLD standard)
- 1800h Fauna Exclusion fencing
- Temporary Construction Fence (1800h chain wire fence with shade cloth)

Vegetation Clearing & Fauna Management Plan - *Detail Sheet Context*

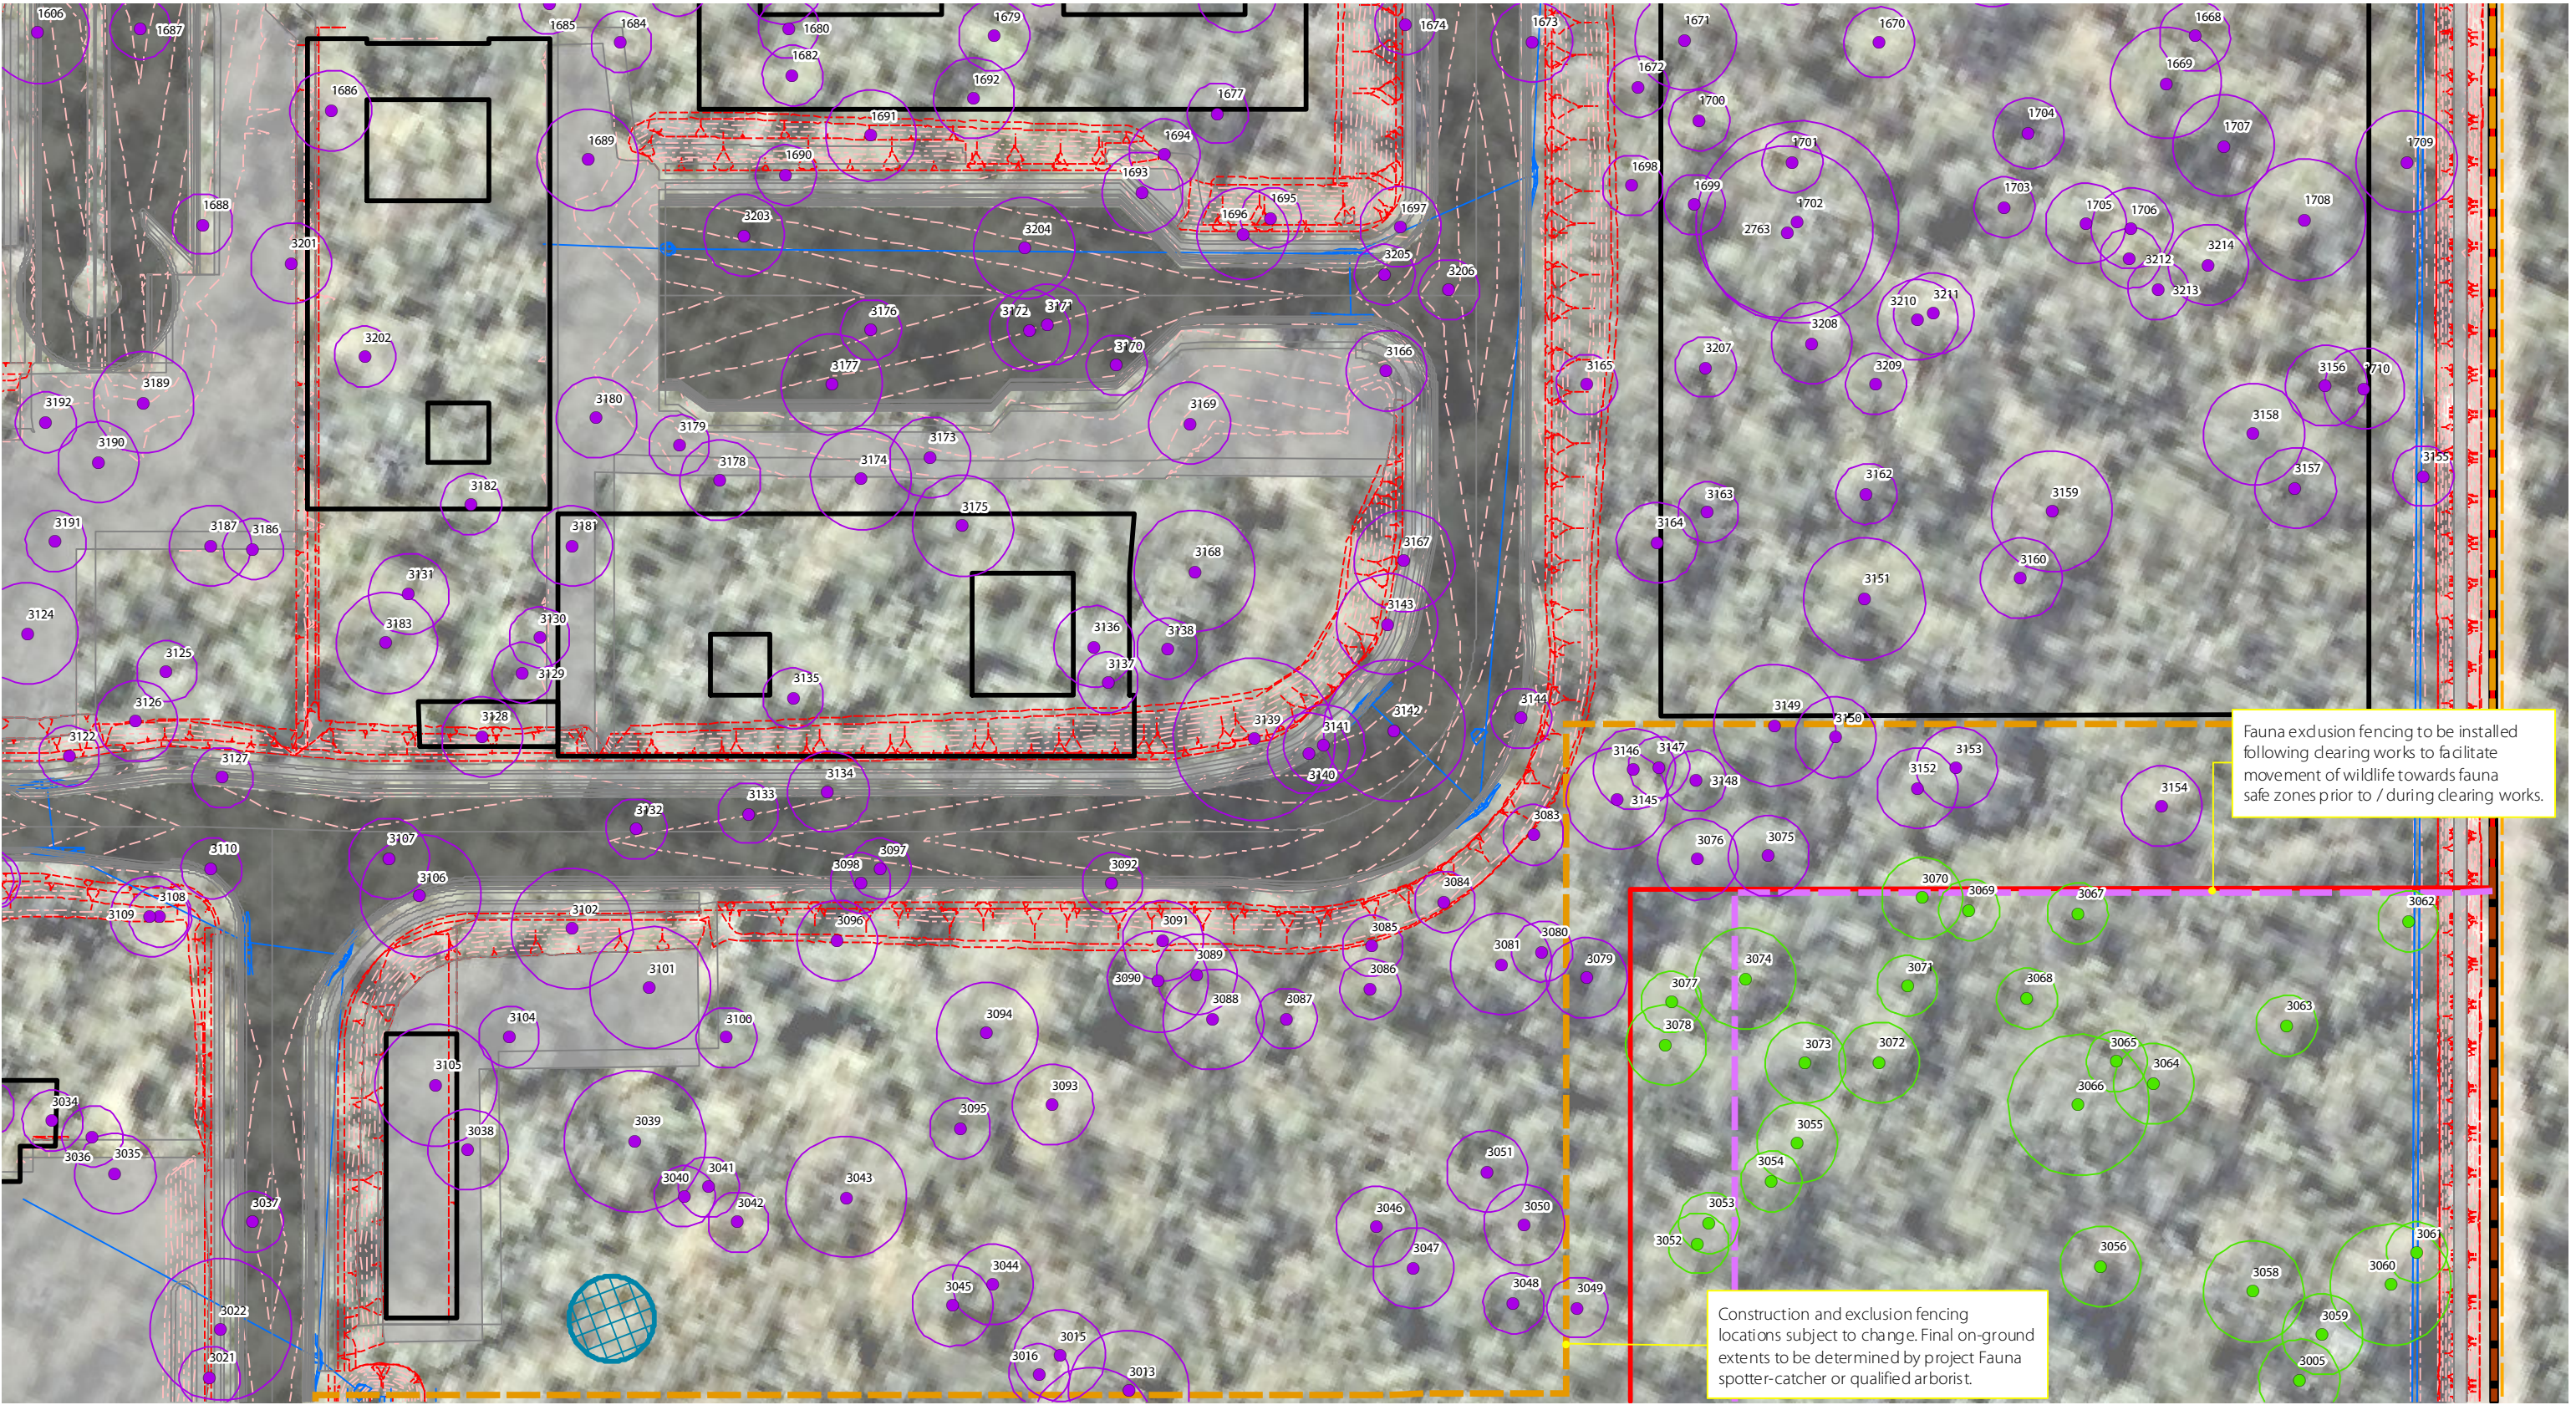

RPS Tree Plot (w/TPZ)

- Tree to retain
- Tree to remove



Disturbance Area

Engineering Detail

- Proposed Buildings
- Proposed Roads
- Proposed Footpaths

Road and Footpath Detail

- Stage Boundaries
- Retaining Walls

Stormwater Design

- Earthworks Batters
- Design Contours

Fencing Locations (External, Indicative)

- 1500h Boundary Fencing - dimbale/fauna-friendly wire fence (replace existing dilapidated log fence)
- 1800h Fence (Energy QLD standard)
- 1800h Fauna Exclusion fencing
- Temporary Construction Fence (1800h chain wire fence with shade cloth)

Vegetation Clearing & Fauna Management Plan - Detail Sheet 09



Client:

Queensland Health

Disclaimer:

THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT. SAUNDERS HAVILL GROUP CANNOT ACCEPT RESPONSIBILITY FOR ANY USE OF OR RELIANCE UPON THE CONTENTS OF THESE DRAWINGS BY ANY THIRD PARTY.

CONFIRM ALL DIMENSIONS ON SITE PRIOR TO CONSTRUCTION AND DO NOT SCALE FROM THE DRAWINGS. ALL DIMENSIONS ARE IN MILLIMETRES. ANY DISCREPANCIES SHOULD BE CLARIFIED IN WRITING WITH SAUNDERS HAVILL GROUP PRIOR TO THE COMMENCEMENT OF WORK.

PRIOR TO ANY DEMOLITION, EXCAVATION OR CONSTRUCTION ON-SITE, THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDERGROUND SERVICES AND DETAILED LOCATIONS OF ALL SERVICES.

References:

Engineering drawing (Stante c, 2023)




Amendments:

Issue	Date	Description	Checked
A	1/1/2023	Client Draft	MD

Project:

Bundaberg Ring Road,
Thabeban




Plan of:
Vegetation Clearing & Fauna Management Plan

Date:	1/1/2023	Checked:	MD
Client Ref:	11612	Drawn:	TF
Drawing No:	11612 E09 VCFMP A		

0 5 10 20 30 40 50 m

1:750 @ A3

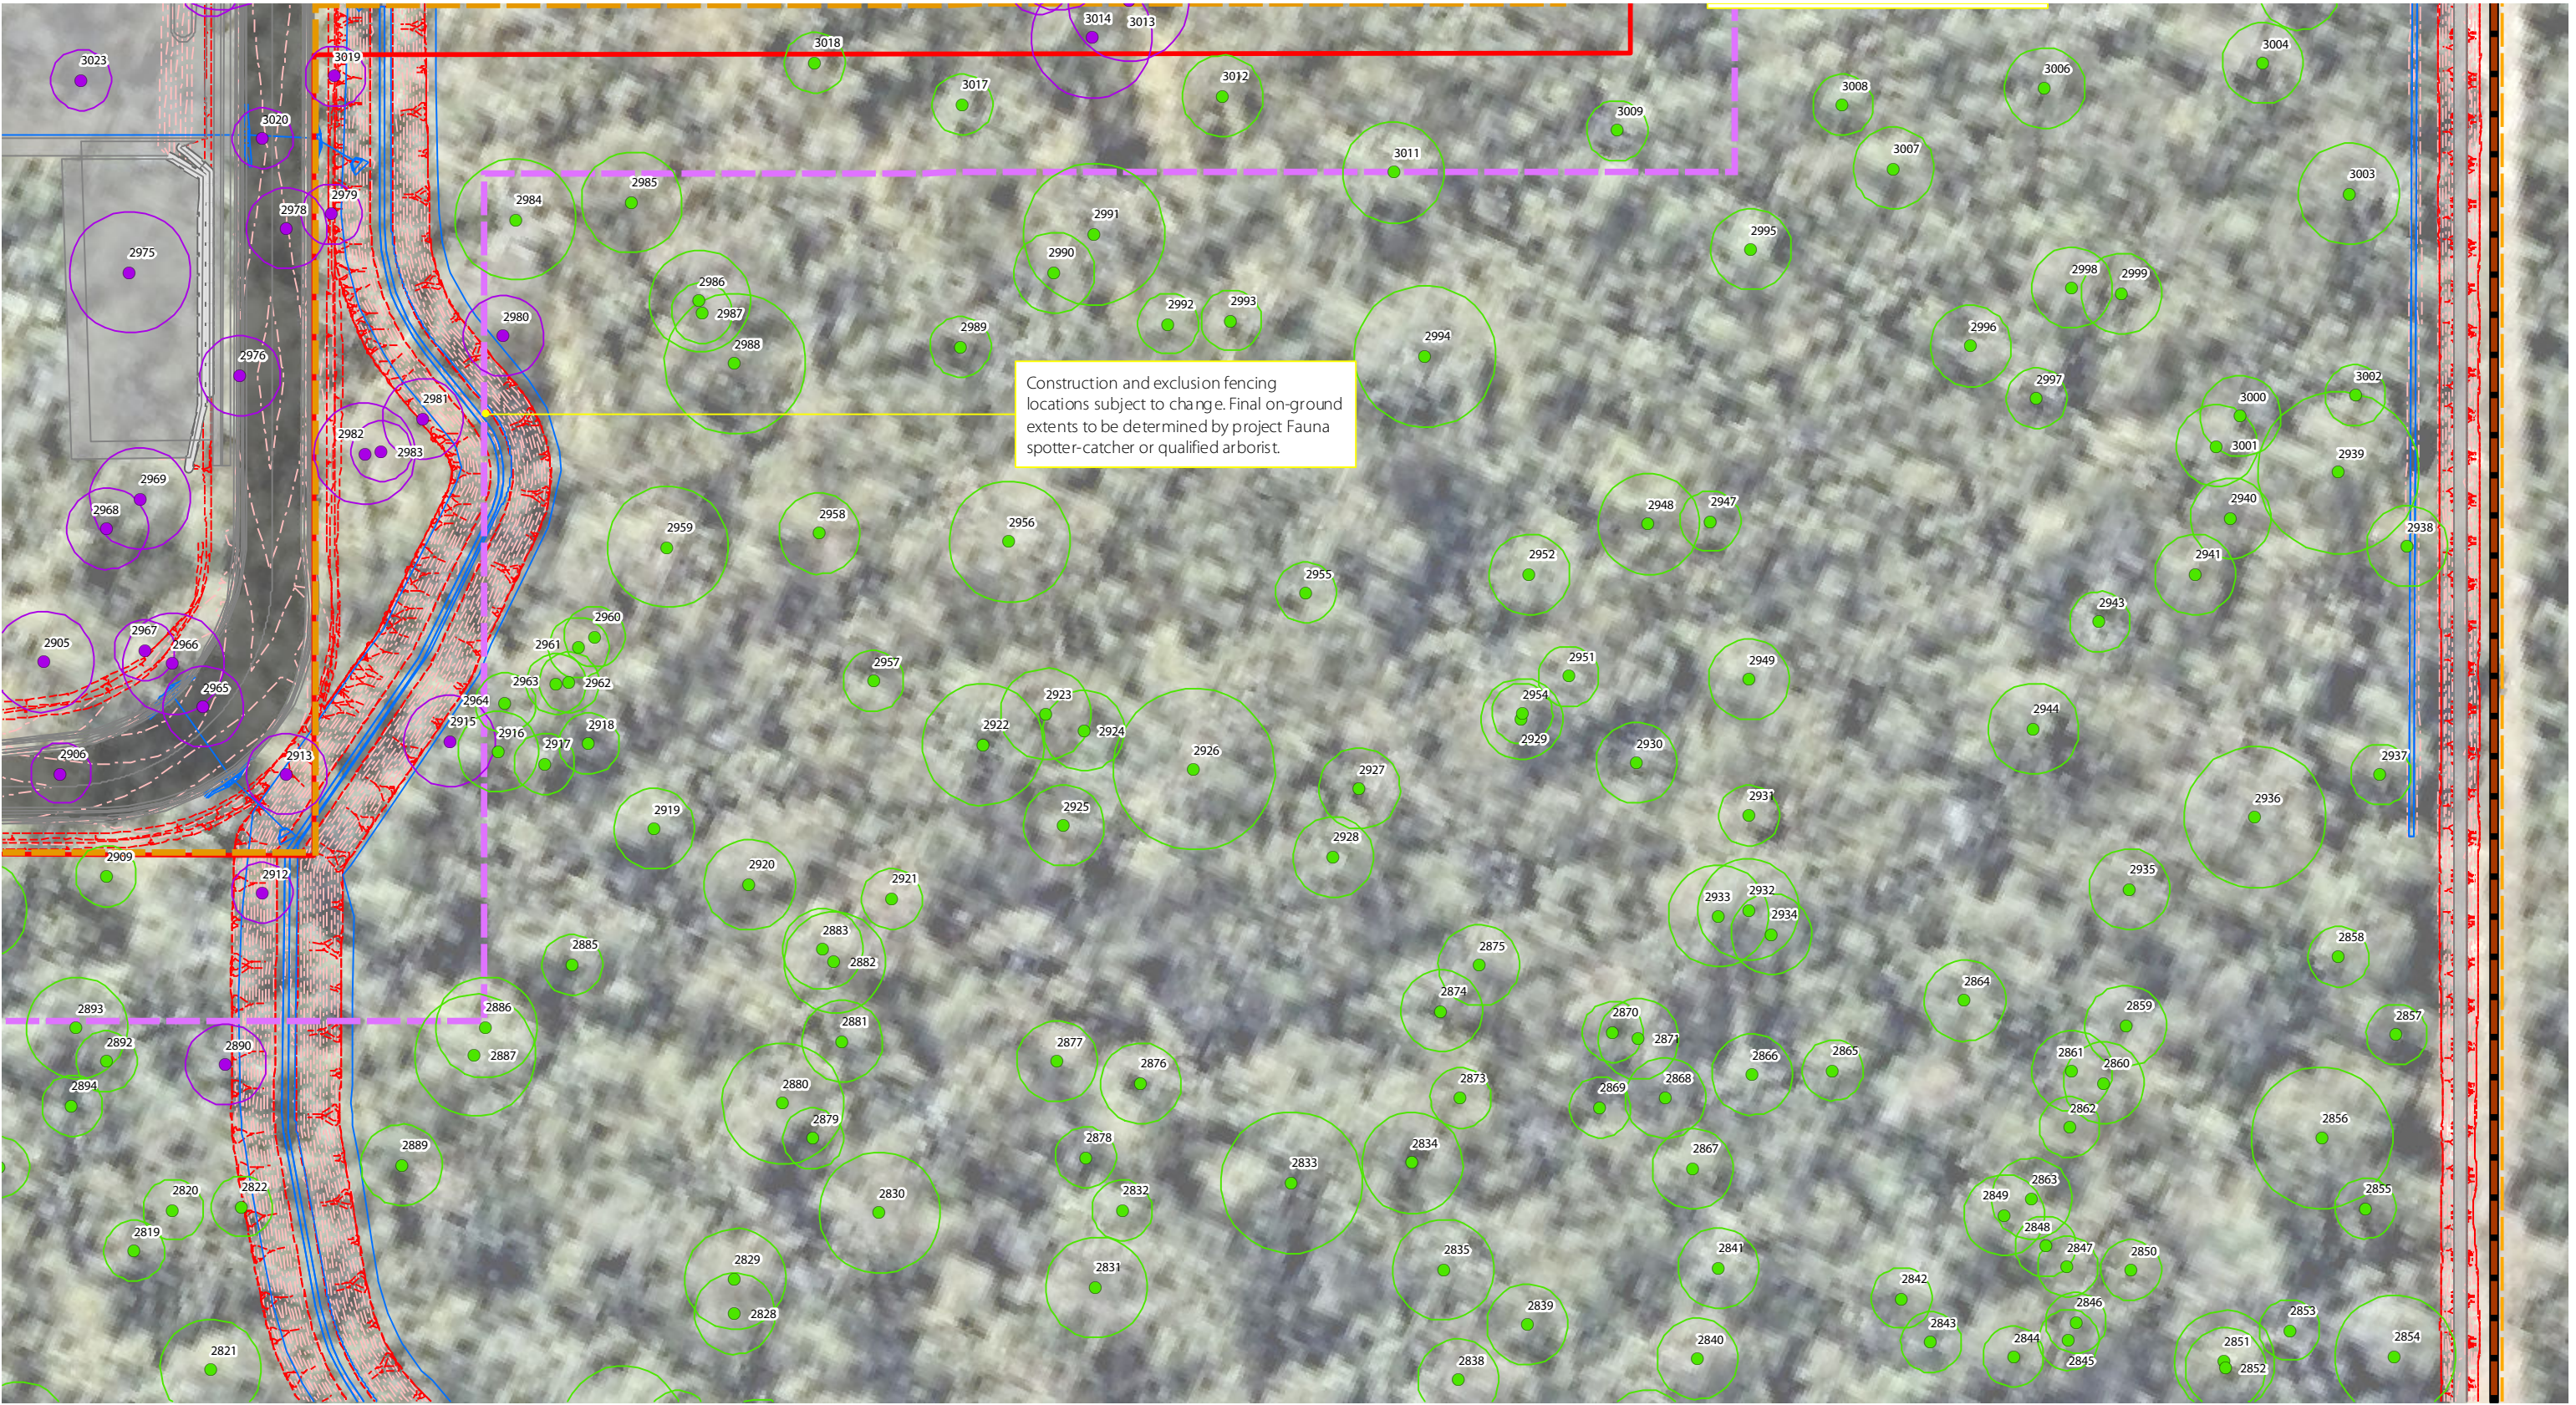

RPS Tree Plot (w/TPZ)
 Tree to retain
 Tree to remove

Engineering Detail
 Proposed Buildings
 Proposed Roads
 Proposed Footpaths


Disturbance Area
 Road and Footpath Detail
 Stage Boundaries
 Retaining Walls

Stormwater Design
 Earthworks Batters
 Design Contours

Fencing Locations (External, Indicative)
 1500h Boundary Fencing - dimbale/fauna-friendly wire fence (replace existing dilapidated log fence)
 1800h Fence (Energy QLD standard)

1800h Fauna Exclusion fencing
 Temporary Construction Fence (1800h chain wire fence with shade cloth)

Vegetation Clearing & Fauna Management Plan - *Detail Sheet 11*

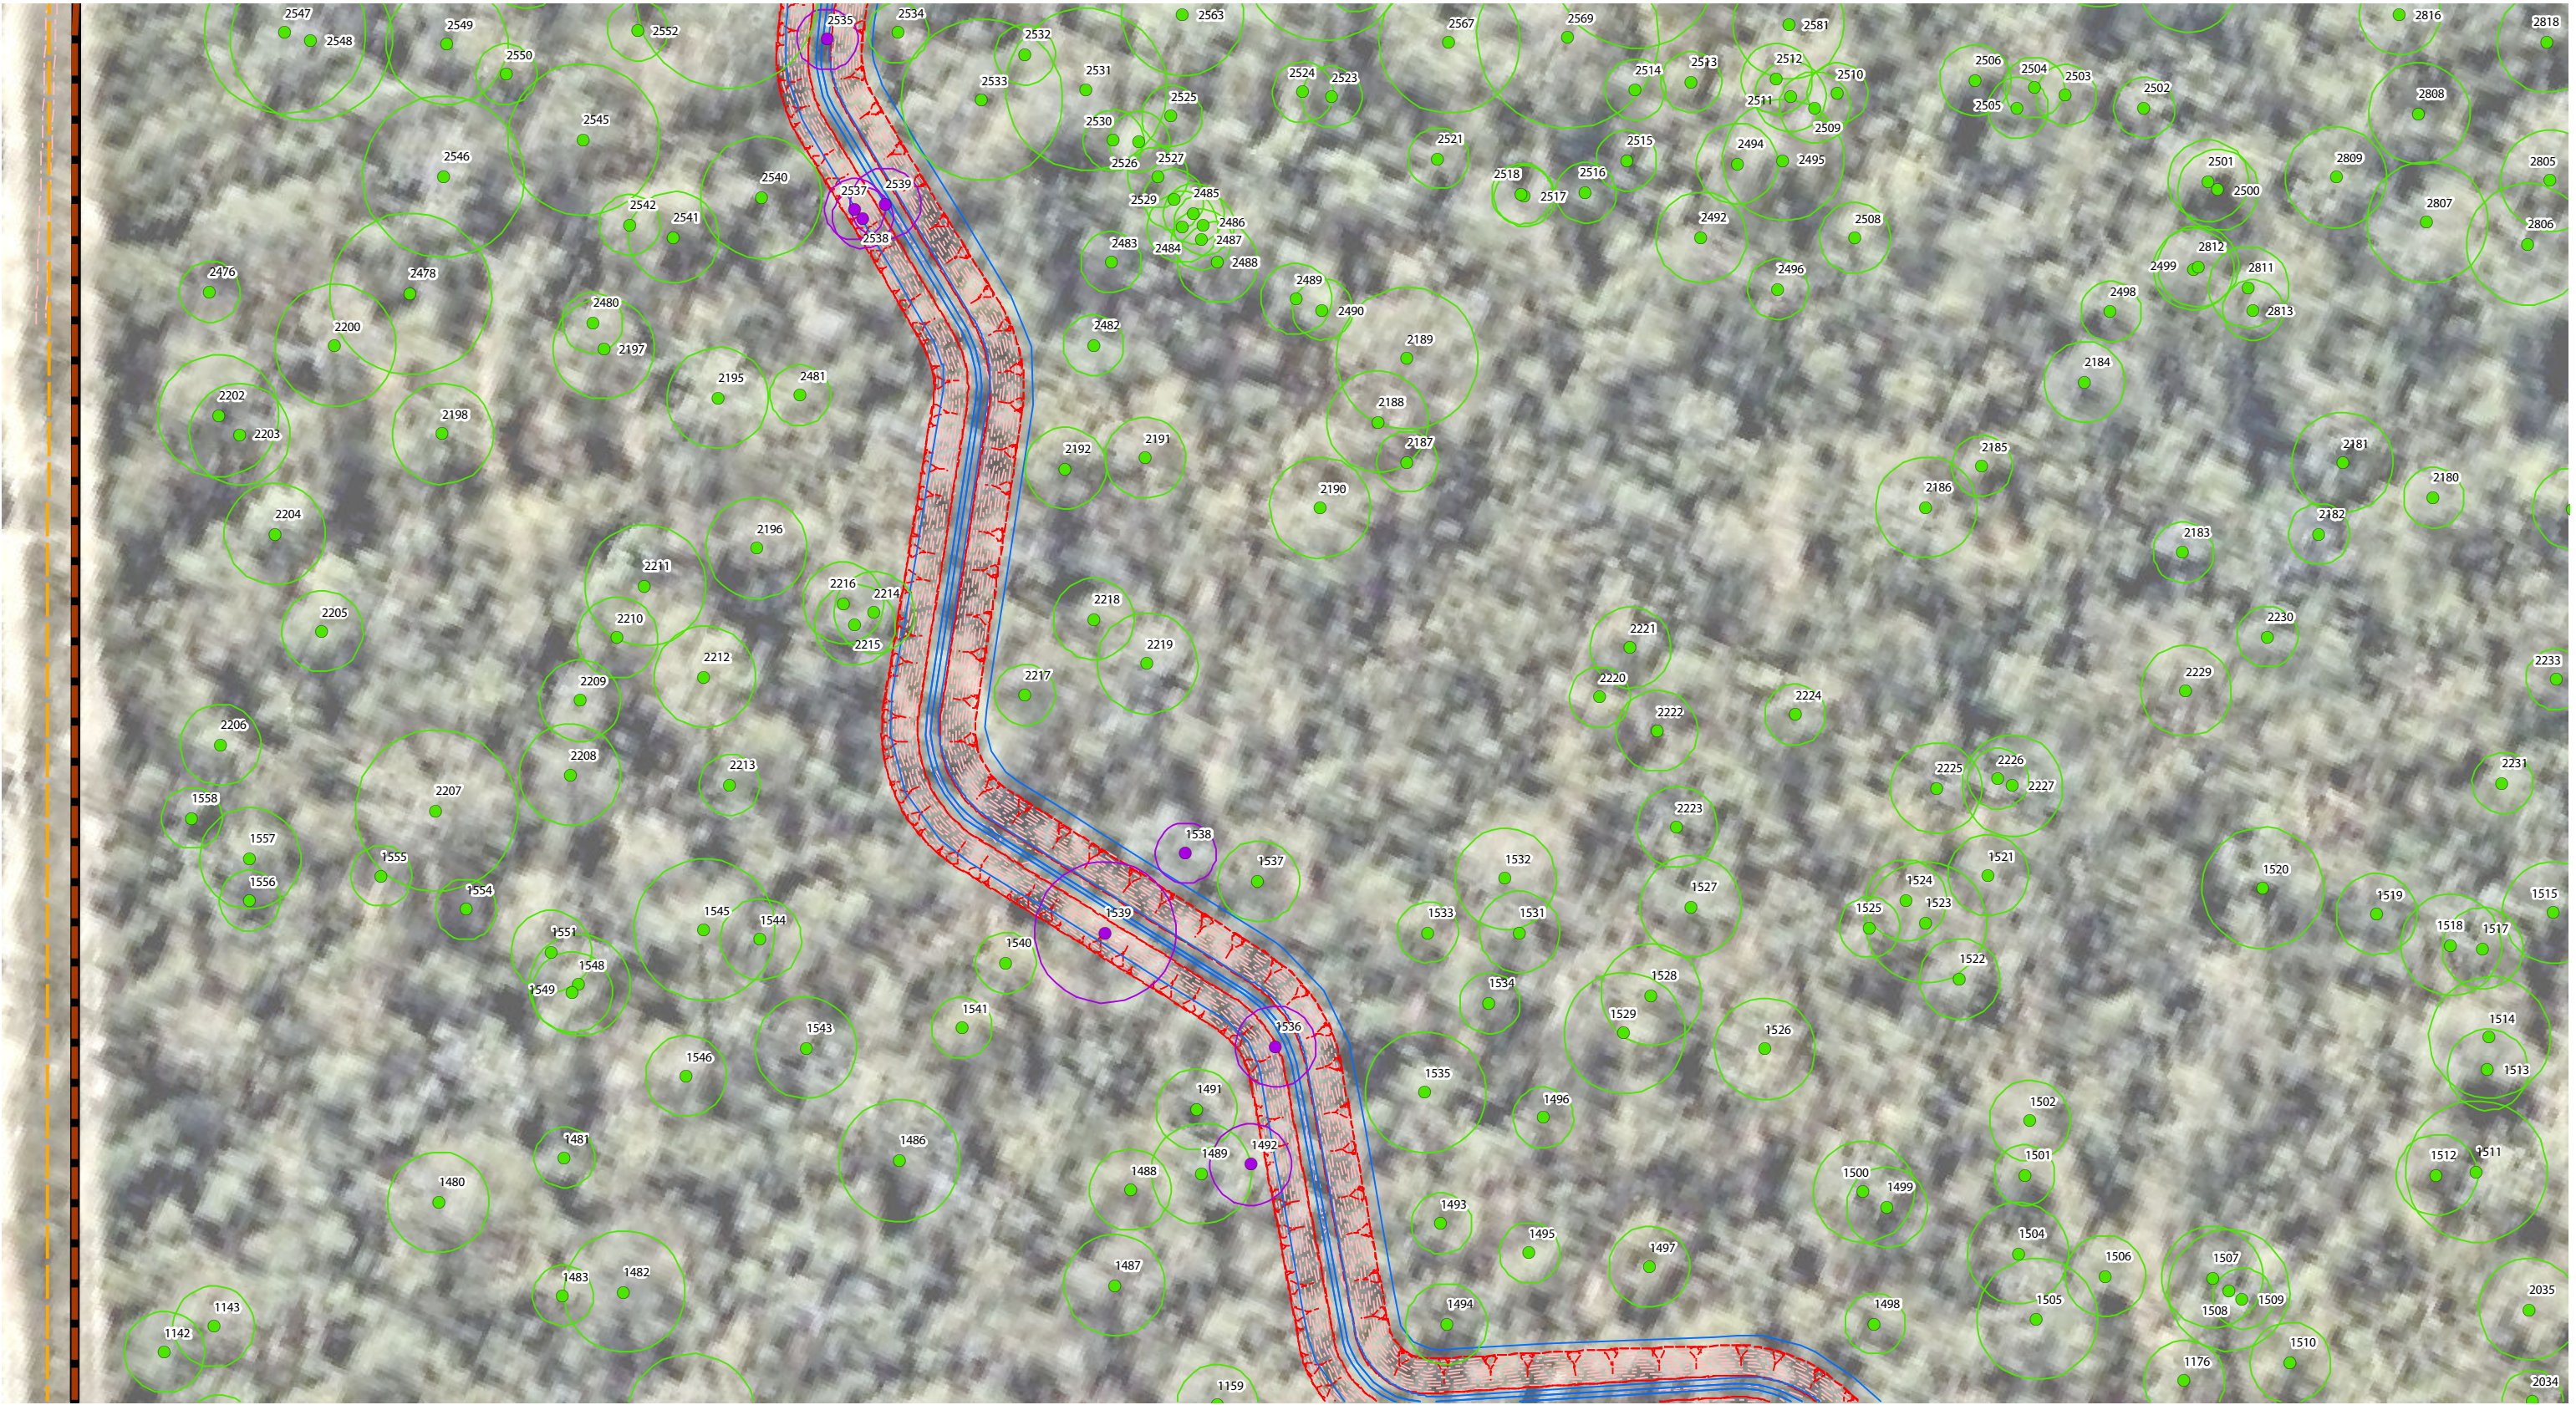

RPS Tree Plot (w/TPZ)
 Tree to retain
 Tree to remove


Engineering Detail
 Disturbance Area
 Proposed Buildings
 Proposed Roads
 Proposed Footpaths

Road and Footpath Detail
 Stage Boundaries
 Retaining Walls

Stormwater Design
 Earthworks Batters
 Design Contours

Fencing Locations (External, Indicative)
 1500h Boundary Fencing - dimbale/fauna-friendly wire fence (replace existing dilapidated log fence)
 1800h Fence (Energy QLD standard)
 1800h Fauna Exclusion fencing
 Temporary Construction Fence (1800h chain wire fence with shade cloth)

Vegetation Clearing & Fauna Management Plan - *Detail Sheet 12*

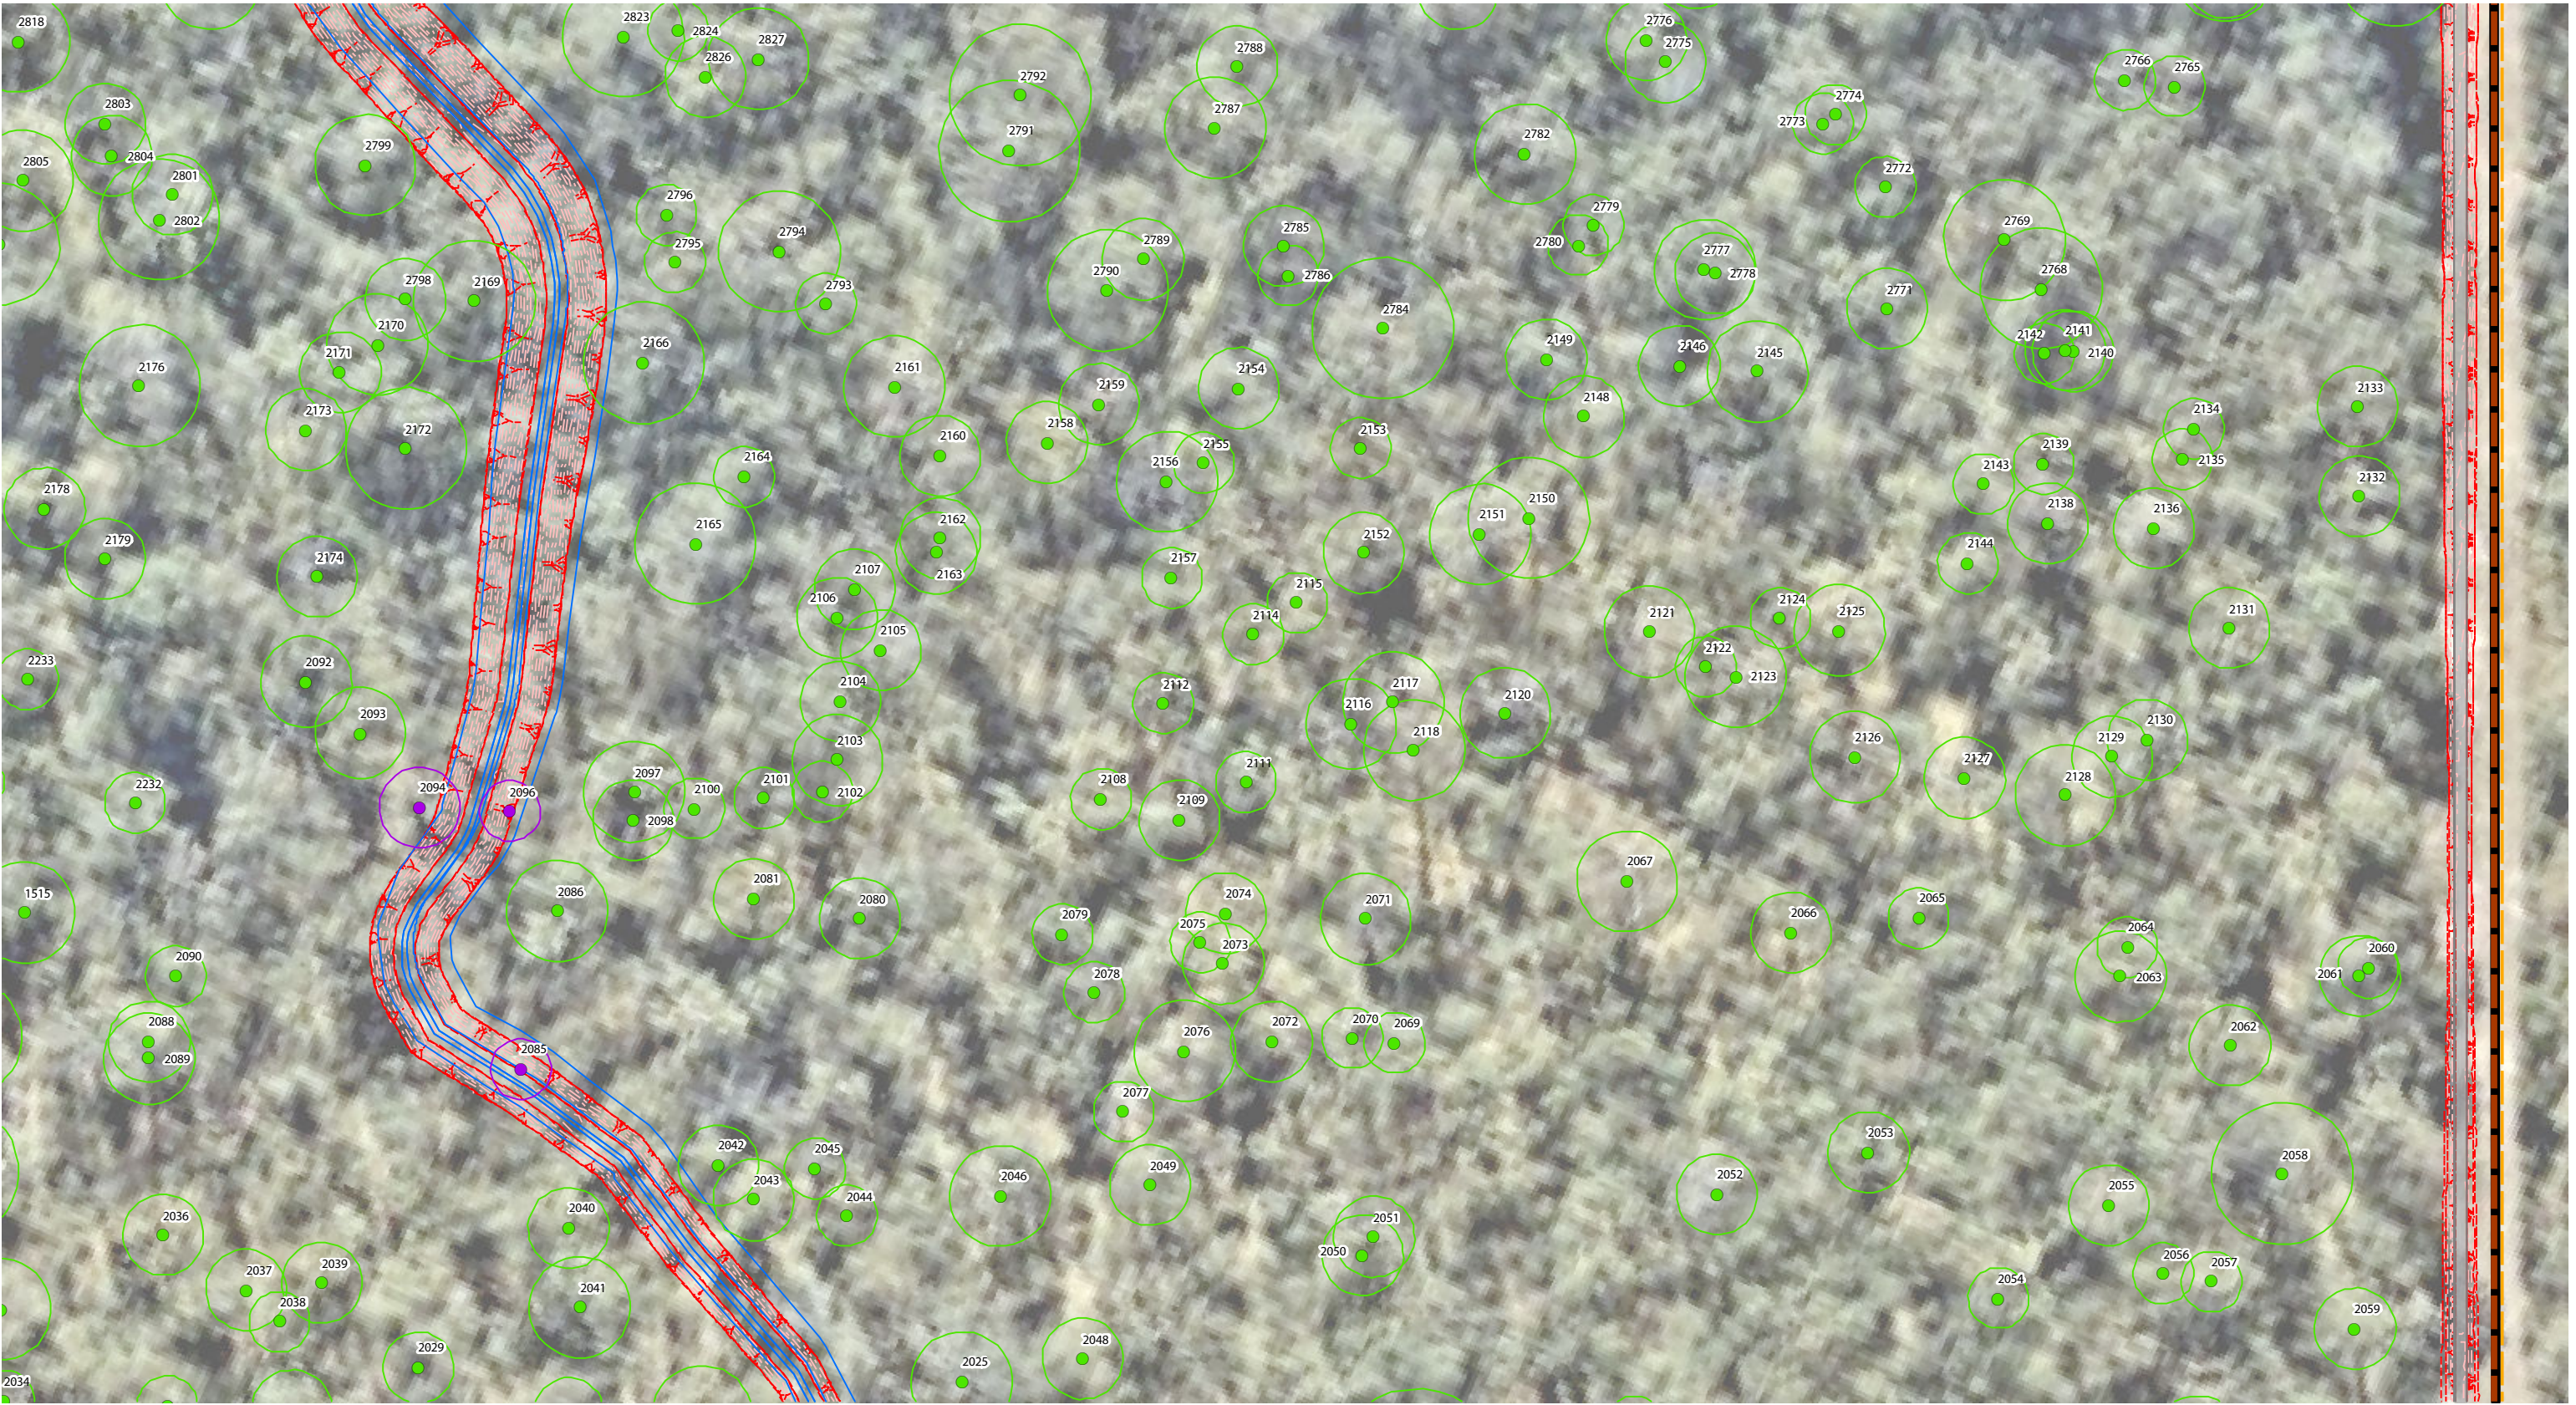

RPS Tree Plot (w/TPZ)
 Tree to retain
 Tree to remove

Engineering Detail
 Disturbance Area
 Proposed Buildings
 Proposed Roads
 Proposed Footpaths

Road and Footpath Detail
 Stage Boundaries
 Retaining Walls

Stormwater Design
 Earthworks Batters
 Design Contours

Fencing Locations (External, Indicative)
 1500h Boundary Fencing - dimbale/fauna-friendly wire fence (replace existing dilapidated log fence)
 1800h Fence (Energy QLD standard)
 1800h Fauna Exclusion fencing
 Temporary Construction Fence (1800h chain wire fence with shade cloth)

Vegetation Clearing & Fauna Management Plan - *Detail Sheet 13*

saunders havill group

Client: Queensland Health

Disclaimer:
THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT. SAUNDERS HAVILL GROUP CANNOT ACCEPT RESPONSIBILITY FOR ANY USE OF OR RELIANCE UP ON THE CONTENTS OF THESE DRAWINGS BY ANY THIRD PARTY.
CONFIRM ALL DIMENSIONS ON SITE PRIOR TO CONSTRUCTION AND DO NOT SCALE FROM THE DRAWINGS. ALL DIMENSIONS ARE IN MILLIMETRES. ANY DISCREPANCIES SHOULD BE CLARIFIED IN WRITING WITH SAUNDERS HAVILL GROUP PRIOR TO THE COMMENCEMENT OF WORK.
PRIOR TO ANY DEMOLITION, EXCAVATION OR CONSTRUCTION ON-SITE, THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDERGROUND SERVICES AND DETAILED LOCATIONS OF ALL SERVICES.

References:
Engineering drawing (Stante c, 2023)

Amendments:

Issue	Date	Description	Checked
A	1/1 1/ 2023	Client Draft	MD

Project:

Bundaberg Ring Road,
Thabeban

Plan of: Vegetation Clearing & Fauna Management Plan

Date: 1/1 1/2023	Checked: MD
Client Ref: 11612	Drawn: TF
Drawing No.: 11612 E13 VCFMP A	

0 5 10 20 30 40 50 m

1:750 @ A3



RPS Tree Plot (w/TPZ)
 Tree to retain
 Tree to remove

Engineering Detail
 Disturbance Area
 Proposed Buildings
 Proposed Roads
 Proposed Footpaths

Road and Footpath Detail
 Stage Boundaries
 Retaining Walls

Stormwater Design
 Earthworks Batters
 Design Contours

Fencing Locations (External, Indicative)
 1500h Boundary Fencing - dimbale/fauna-friendly wire fence (replace existing dilapidated log fence)
 1800h Fence (Energy QLD standard)

1800h Fauna Exclusion fencing
 Temporary Construction Fence (1800h chain wire fence with shade cloth)

saunders havill group

Client: Queensland Health

Disclaimer:
THESE PLANS HAVE BEEN PREPARED FOR THE EXCLUSIVE USE OF THE CLIENT. SAUNDERS HAVILL GROUP CANNOT ACCEPT RESPONSIBILITY FOR ANY USE OF OR RELIANCE UPON THE CONTENTS OF THESE DRAWINGS BY ANY THIRD PARTY.
CONFIRM ALL DIMENSIONS ON SITE PRIOR TO CONSTRUCTION AND DO NOT SCALE FROM THE DRAWINGS. ALL DIMENSIONS ARE IN MILLIMETRES. ANY DISCREPANCIES SHOULD BE CLARIFIED IN WRITING WITH SAUNDERS HAVILL GROUP PRIOR TO THE COMMENCEMENT OF WORK.
PRIOR TO ANY DEMOLITION, EXCAVATION OR CONSTRUCTION ON-SITE, THE RELEVANT AUTHORITY SHOULD BE CONTACTED FOR FURTHER UNDERGROUND SERVICES AND DETAILED LOCATIONS OF ALL SERVICES.

References:
Engineering drawing (Stante c, 2023)

Amendments:
Issue Date Description Checked
A 1/1 1/2023 Client Draft MD

0 5 10 20 30 40 50 m
1:750 @ A3


Project: Bundaberg Ring Road, Thabeban

environmental management

Plan of: Vegetation Clearing & Fauna Management Plan

Date: 1/1 1/2023 Checked: MD
Client Ref: 11612 Drawn: TF
Drawing No.: 11612 E15 VCFMP A

Vegetation Clearing & Fauna Management Plan - Detail Sheet 15

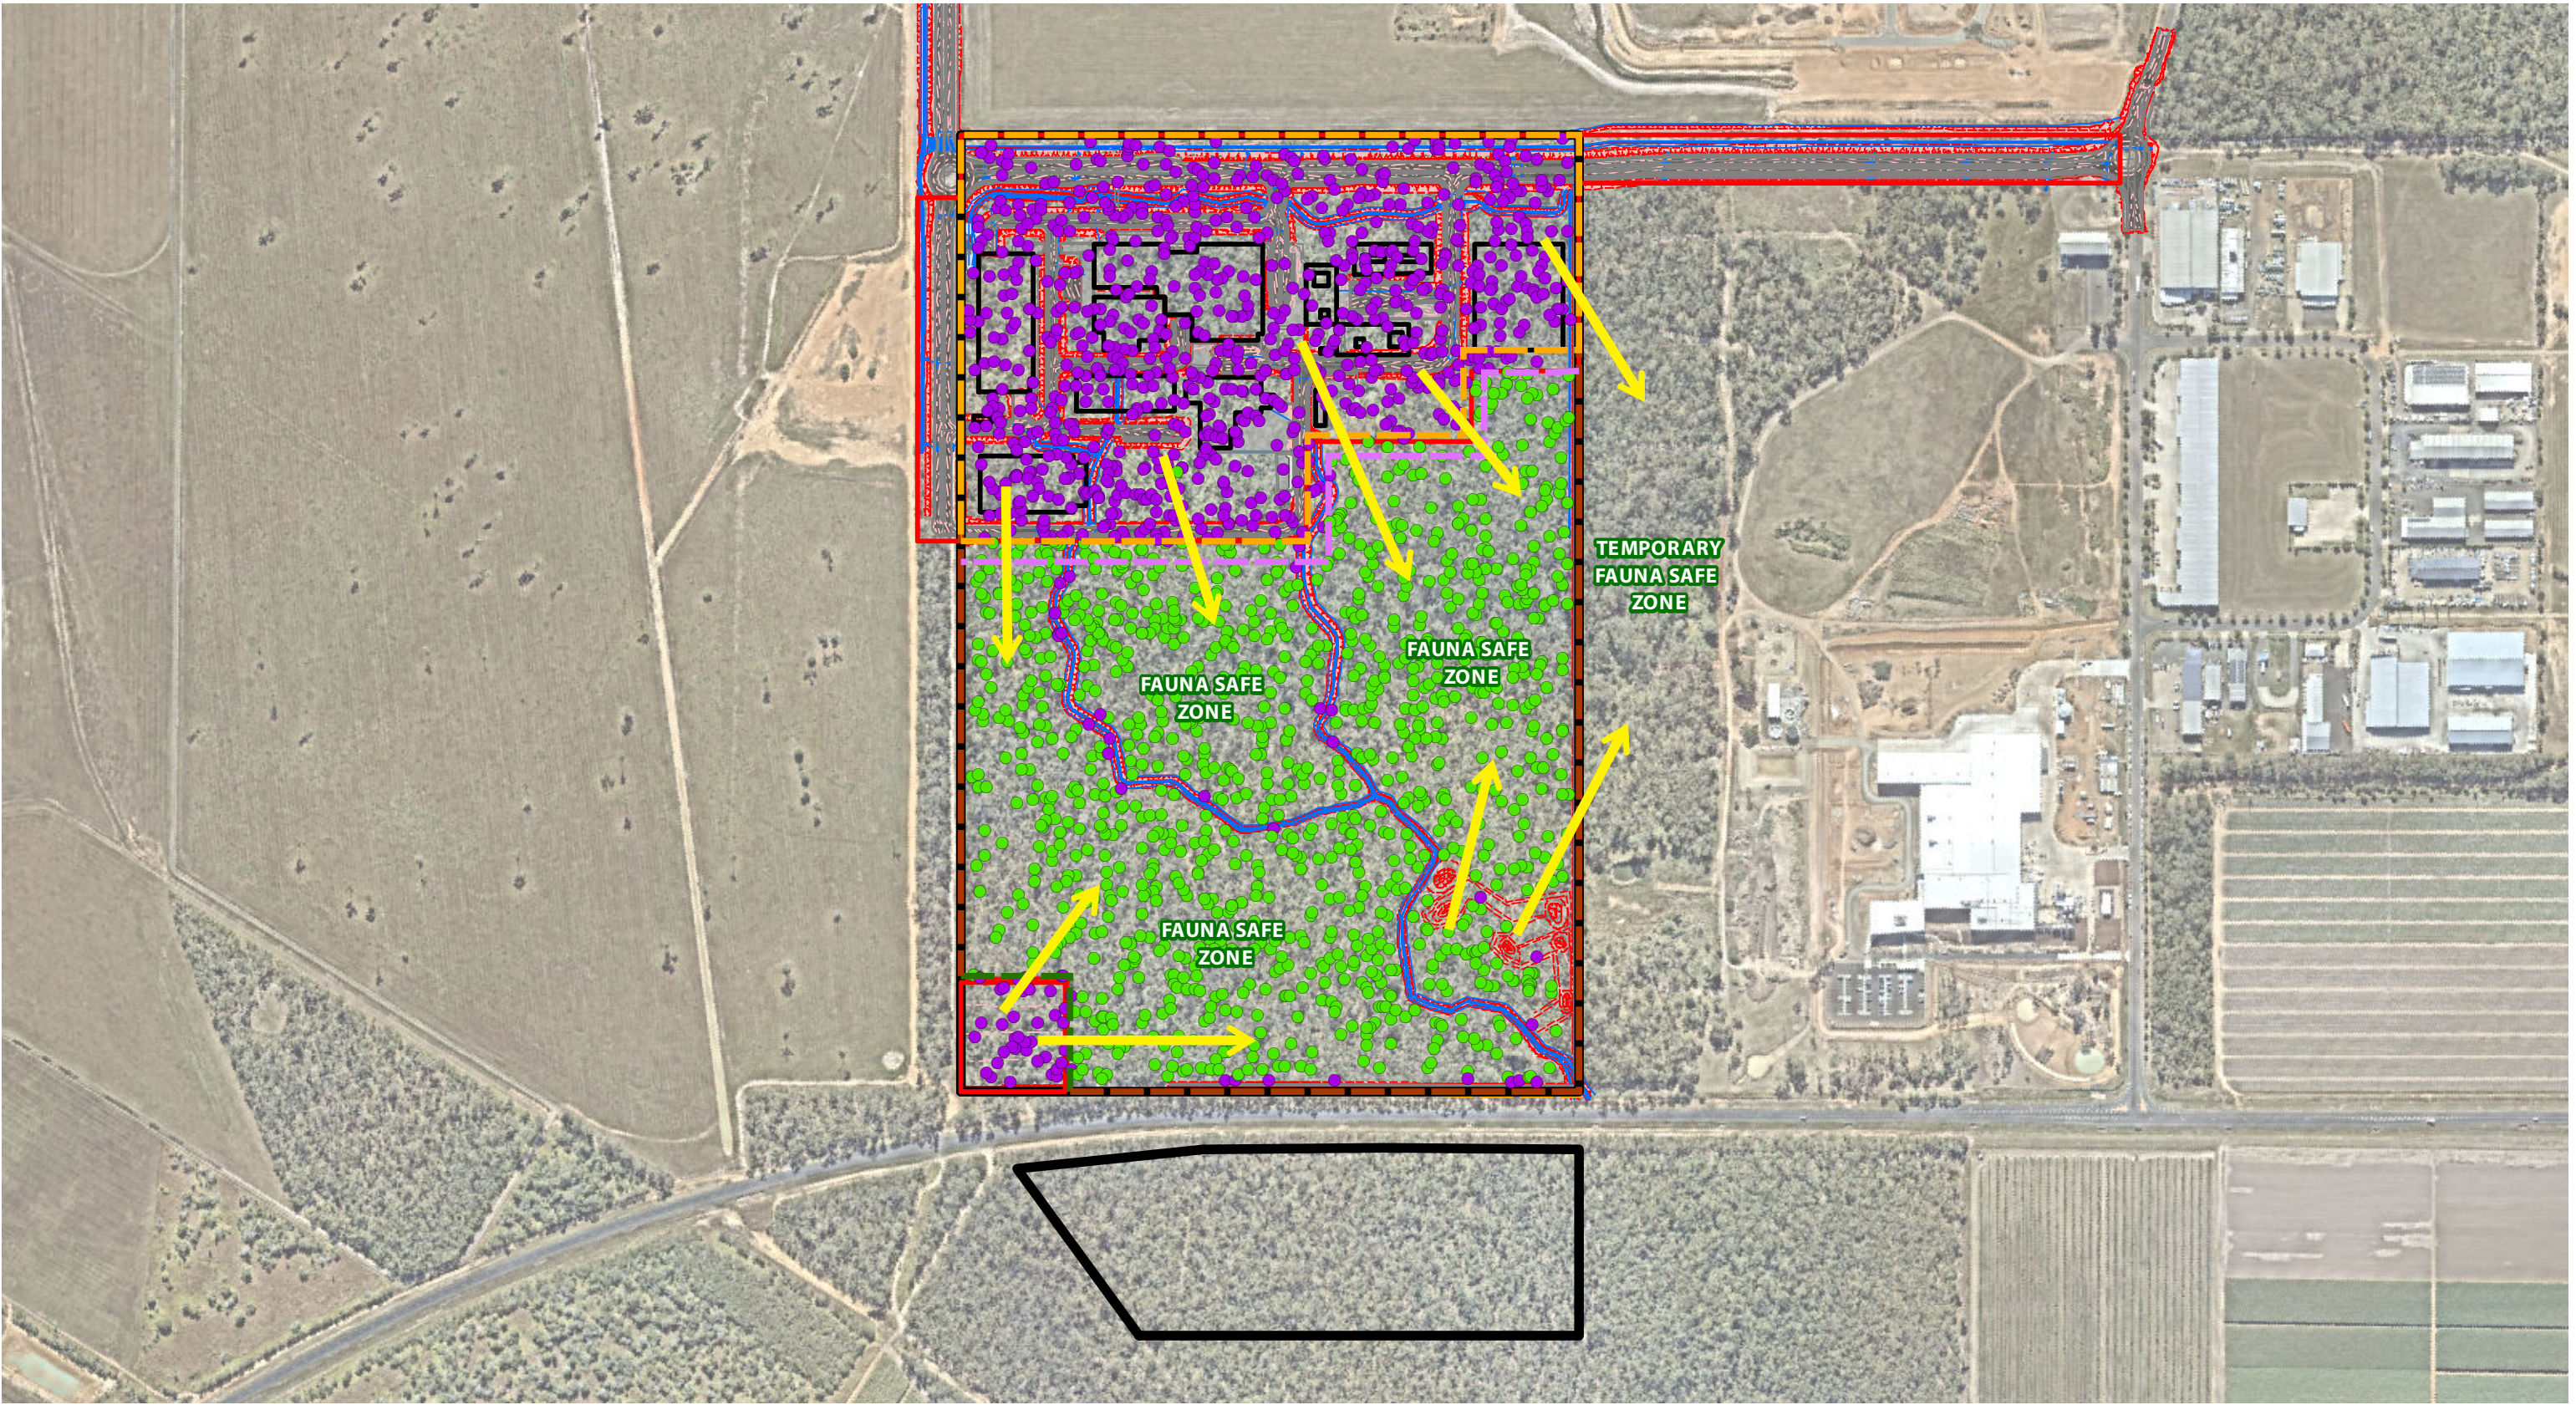

RPS Tree Plot

- Tree to retain
- Tree to retain subject to detailed stormwater design
- Tree to remove

Engineering Detail

- ▭ Disturbance Area
- ▭ Proposed Buildings
- ▭ Proposed Roads
- ▭ Proposed Footpaths

— Road and Footpath Detail

— Stage Boundaries

▭ Retaining Walls

— Stormwater Design

--- Earthworks Batters

--- Design Contours

Fencing Locations (External, Indicative)

- 1500h Boundary Fencing - dimbale/fauna-friendly wire fence (replace existing dilapidated log fence)
- 1800h Fence (Energy QLD standard)
- 1800h Fauna Exclusion fencing
- Temporary Construction Fence (1800h chain wire fence with shade cloth)

← Clearing direction (indicative)

Vegetation Clearing & Fauna Management Plan - *Clearing Direction*



Specimen Details						
Tree ID	Tree Type	Spread (m)	Height (m)	DBH (mm)	TPZ (m)	Retention
1000	Gum	5	15	300	4	Remove
1001	Gum	5	15	300	4	Remove
1002	Gum	5	15	300	4	Remove
1003	Gum	10	15	320	4	Remove
1004	Gum	6	15	450	5	Remove
1005	Gum	6	15	300	4	Remove
1006	Gum	10	15	300	4	Remove
1007	Gum	10	20	700	8	Remove
1008	Gum	7	15	350	4	Remove
1009	Gum	7	15	350	4	Remove
1010	Gum	5	15	350	4	Remove
1011	Ironbark	6	15	300	4	Remove
1012	Gum	6	15	300	4	Remove
1013	Gum	10	20	500	6	Remove
1014	Gum	5	15	400	5	Remove
1015	Gum	10	15	500	6	Remove
1016	Gum	5	15	300	4	Remove
1017	Gum	5	15	320	4	Remove
1018	Gum	10	15	370	4	Remove
1019	Gum	6	15	350	4	Remove
1020	Gum	6	15	350	4	Remove
1021	Gum	12	20	550	7	Remove
1022	Gum	6	20	400	5	Remove
1023	Gum	6	15	350	4	Remove
1024	Gum	6	15	300	4	Remove
1025	Gum	6	15	400	5	Remove
1026	Gum	6	15	300	4	Remove

Specimen Details						
Tree ID	Tree Type	Spread (m)	Height (m)	DBH (mm)	TPZ (m)	Retention
1027	Gum	10	15	500	6	Remove
1028	Gum	5	15	400	5	Remove
1029	Gum	4	15	350	4	Remove
1030	Gum	5	15	320	4	Remove
1031	Gum	2	15	300	4	Remove
1032	Gum	10	15	450	5	Remove
1033	Gum	6	15	300	4	Remove
1034	Gum	6	15	300	4	Remove
1035	Gum	6	15	450	5	Remove
1036	Gum	6	15	350	4	Remove
1037	Gum	5	15	300	4	Remove
1038	Gum	10	15	300	4	Remove
1039	Gum	10	15	450	5	Remove
1040	Gum	6	15	300	4	Remove
1041	Gum	12	20	550	7	Remove
1042	Gum	6	15	500	6	Remove
1043	Gum	6	15	400	5	Remove
1044	Gum	8	15	300	4	Remove
1045	Gum	8	15	300	4	Remove
1046	Gum	6	15	300	4	Remove
1047	Gum	6	15	400	5	Remove
1048	Gum	8	15	350	4	Remove
1049	Gum	8	15	300	4	Remove
1050	Gum	10	15	400	5	Remove
1051	Gum	6	15	300	4	Remove
1052	Paperbark	15	15	300	4	Remove
1053	Gum	6	15	300	4	Remove
1054	Gum	8	15	350	4	Remove
1055	Paperbark	6	15	300	4	Remove
1056	Paperbark	10	15	300	4	Remove

Specimen Details						
Tree ID	Tree Type	Spread (m)	Height (m)	DBH (mm)	TPZ (m)	Retention
1057	Gum	10	15	400	5	Remove
1058	Gum	15	15	450	5	Remove
1059	Gum	10	15	300	4	Remove
1060	Gum	10	15	300	4	Remove
1061	Gum	8	15	300	4	Remove
1062	Gum	10	15	300	4	Remove
1063	Gum	10	15	400	5	Remove
1064	Gum	12	15	400	5	Remove
1065	Gum	10	15	300	4	Remove
1066	Gum	8	15	300	4	Remove
1067	Gum	10	15	350	4	Remove
1068	Gum	12	15	400	5	Remove
1069	Gum	10	15	450	5	Remove
1070	Gum	10	15	450	5	Remove
1071	Gum	8	15	300	4	Remove
1072	Gum	10	15	450	5	Remove
1073	Gum	15	15	500	6	Remove
1074	Gum	8	15	400	5	Remove
1075	Gum	10	15	350	4	Remove
1076	Gum	10	15	350	4	Remove
1077	Gum	10	15	450	5	Remove
1078	Gum	10	15	350	4	Remove
1079	Gum	10	15	350	4	Remove
1080	Gum	10	15	300	4	Remove
1081	Gum	10	15	350	4	Remove
1082	Gum	8	15	400	5	Remove
1083	Gum	8	15	300	4	Remove
1084	Gum	10	15	350	4	Remove
1085	Gum	10	15	350	4	Remove
1086	Gum	8	15	300	4	Remove

Specimen Details						
Tree ID	Tree Type	Spread (m)	Height (m)	DBH (mm)	TPZ (m)	Retention
1087	Gum	10	15	450	5	Remove
1088	Gum	10	15	300	4	Remove
1089	Gum	10	15	300	4	Remove
1090	Gum	8	15	350	4	Remove
1091	Gum	8	15	300	4	Remove
1092	Gum	8	15	300	4	Remove
1093	Gum	10	15	400	5	Remove
1094	Gum	10	15	400	5	Remove
1095	Gum	15	15	450	5	Remove
1096	Gum	10	15	400	5	Remove
1097	Gum	10	15	300	4	Remove
1098	Gum	6	15	300	4	Remove
1099	Gum	6	15	300	4	Remove
1100	Gum	10	15	500	6	Remove
1101	Gum	10	15	300	4	Remove
1102	Gum	15	15	500	6	Remove
1103	Gum	10	15	300	4	Remove
1104	Gum	10	15	300	4	Remove
1105	Gum	10	15	300	4	Remove
1106	Gum	10	15	350	4	Remove
1107	Gum	15	15	400	5	Remove
1108	Gum	6	15	400	5	Remove
1109	Gum	10	15	500	6	Remove
1110	Gum	10	15	400	5	Remove
1111	Gum	10	15	300	4	Remove
1112	Gum	6	15	350	4	Remove
1113	Gum	10	15	350	4	Remove
1114	Gum	15	15	600	7	Remove
1115	Gum	6	20	450	5	Remove
1116	Gum	6	20	350	4	Remove

Specimen Details						
Tree ID	Tree Type	Spread (m)	Height (m)	DBH (mm)	TPZ (m)	Retention
1117	Gum	8	20	400	5	Remove
1118	Gum	8	15	300	4	Remove
1119	Gum	8	15	300	4	Remove
1120	Gum	15	20	500	6	Remove
1121	Gum	10	15	350	4	Remove
1122	Gum	10	15	300	4	Remove
1123	Gum	15	20	550	7	Remove
1124	Gum	6	15	300	4	Remove
1125	Gum	10	15	450	5	Remove
1126	Gum	15	15	300	4	Remove
1127	Gum	10	15	300	4	Remove
1128	Gum	10	20	300	4	Remove
1129	Gum	15	20	550	7	Remove
1130	Gum	15	20	550	7	Remove
1131	Gum	15	20	400	5	Remove
1132	Gum	10	15	350	4	Remove
1133	Gum	10	15	350	4	Remove
1134	Gum	10	15	400	5	Remove
1135	Gum	15	20	500	6	Remove
1136	Gum	10	15	300	4	Remove
1137	Gum	10	15	300	4	Remove
1138	Gum	10	15	300	4	Remove
1139	Gum	10	15	300	4	Remove
1140	Gum	8	15	300	4	Remove
1142	Gum	7	20	400	5	Retain
1143	Gum	7	20	400	5	Retain
1144	Gum	10	20	400	5	Retain
1145	Paperbark	3	10	300	4	Retain
1146	Gum	15	20	500	6	Retain
1147	Native	3	10	300	4	Retain

Specimen Details						
Tree ID	Tree Type	Spread (m)	Height (m)	DBH (mm)	TPZ (m)	Retention
1148	Gum	15	25	650	8	Retain
1149	Gum	10	25	600	7	Retain
1150	Gum	10	20	400	5	Retain
1151	Gum	10	20	500	6	Retain
1152	Gum	10	15	300	4	Retain
1153	Gum	10	20	400	5	Retain
1154	Gum	5	15	300	4	Retain
1155	Gum	15	25	500	6	Retain
1156	Gum	5	15	300	4	Retain
1157	Gum	5	15	350	4	Retain
1158	Gum	10	15	350	4	Retain
1159	Gum	10	20	400	5	Retain
1160	Gum	15	25	500	6	Retain
1161	Gum	15	20	400	5	Remove
1163	Gum	10	25	400	5	Retain
1164	Gum	10	20	300	4	Retain
1165	Gum	10	20	300	4	Retain
1166	Gum	10	20	350	4	Retain
1168	Gum	20	30	700	8	Retain
1170	Gum	5	15	300	4	Retain
1171	Gum	10	30	400	5	Retain
1172	Gum	10	15	300	4	Remove
1174	Gum	10	15	300	4	Retain
1175	Gum	10	15	350	4	Retain
1176	Gum	10	20	400	5	Retain
1178	Gum	10	25	400	5	Retain
1179	Gum	10	20	350	4	Retain
1180	Gum	15	25	400	5	Retain
1181	Gum	10	20	300	4	Retain
1182	Gum	10	20	300	4	Retain

Specimen Details						
Tree ID	Tree Type	Spread (m)	Height (m)	DBH (mm)	TPZ (m)	Retention
1184	Gum	15	30	600	7	Retain
1185	Gum	15	30	500	6	Retain
1186	Gum	15	25	400	5	Retain
1187	Gum	15	30	700	8	Retain
1188	Gum	10	20	300	4	Retain
1189	Gum	5	15	300	4	Retain
1190	Gum	10	30	450	5	Retain
1191	Gum	5	15	300	4	Retain
1192	Gum	10	20	400	5	Retain
1193	Gum	5	15	300	4	Retain
1194	Gum	5	15	300	4	Retain
1195	Gum	5	15	300	4	Retain
1196	Gum	10	20	300	4	Retain
1197	Gum	10	20	300	4	Retain
1198	Gum	10	30	600	7	Retain
1201	Gum	10	30	450	5	Retain
1202	Gum	10	30	500	6	Retain
1203	Gum	10	30	400	5	Retain
1204	Gum	10	20	400	5	Retain
1205	Gum	10	20	400	5	Retain
1206	Gum	10	20	450	5	Retain
1207	Gum	10	20	450	5	Retain
1208	Gum	15	20	550	7	Retain
1209	Gum	10	20	300	4	Retain
1210	Gum	5	15	300	4	Retain
1212	Gum	10	20	350	4	Retain
1215	Gum	15	30	600	7	Retain
1216	Gum	15	30	500	6	Retain
1217	Gum	15	30	500	6	Retain
1218	Gum	5	10	300	4	Retain

Specimen Details						
Tree ID	Tree Type	Spread (m)	Height (m)	DBH (mm)	TPZ (m)	Retention
1219	Gum	5	15	400	5	Retain
1220	Paperbark	10	15	300	4	Retain
1221	Gum	10	15	350	4	Retain
1222	Gum	10	20	350	4	Retain
1223	Gum	15	30	500	6	Retain
1224	Gum	15	30	600	7	Retain
1225	Gum	10	30	400	5	Retain
1226	Gum	10	20	300	4	Retain
1227	Gum	10	20	300	4	Retain
1228	Gum	10	15	450	5	Retain
1229	Gum	15	30	500	6	Retain
1230	Gum	15	30	500	6	Retain
1231	Gum	15	25	400	5	Retain
1232	Gum	15	30	600	7	Retain
1233	Gum	12	20	300	4	Retain
1234	Gum	10	25	400	5	Retain
1235	Gum	10	25	400	5	Retain
1236	Gum	10	25	300	4	Retain
1237	Gum	10	25	300	4	Retain
1239	Gum	10	20	300	4	Retain
1241	Gum	20	25	600	7	Retain
1242	Gum	5	20	300	4	Retain
1243	Gum	10	30	400	5	Retain
1244	Gum	10	30	400	5	Retain
1245	Gum	15	25	400	5	Retain
1246	Gum	15	30	400	5	Retain
1247	Gum	5	15	300	4	Retain
1248	Gum	5	15	300	4	Retain
1249	Gum	5	15	300	4	Retain
1250	Gum	15	25	500	6	Retain

Specimen Details						
Tree ID	Tree Type	Spread (m)	Height (m)	DBH (mm)	TPZ (m)	Retention
1251	Gum	15	20	500	6	Retain
1252	Gum	10	25	400	5	Retain
1254	Gum	10	20	300	4	Retain
1255	Gum	10	25	400	5	Retain
1256	Gum	5	15	300	4	Retain
1257	Gum	15	30	400	5	Retain
1260	Gum	15	30	600	7	Retain
1262	Gum	15	30	600	7	Retain
1263	Tree	5	25	500	6	Retain
1264	Gum	15	30	600	7	Retain
1265	Gum	15	30	600	7	Retain
1266	Gum	15	30	600	7	Retain
1267	Gum	10	30	400	5	Retain
1268	Gum	10	25	400	5	Retain
1270	Gum	15	30	500	6	Retain
1271	Gum	15	30	500	6	Retain
1272	Gum	10	20	300	4	Retain
1273	Gum	10	20	300	4	Retain
1274	Gum	10	20	300	4	Retain
1275	Gum	10	20	300	4	Retain
1276	Gum	10	30	400	5	Retain
1277	Gum	15	30	600	7	Retain
1278	Gum	10	20	300	4	Retain
1279	Gum	15	25	400	5	Retain
1280	Gum	5	20	300	4	Retain
1281	Gum	5	20	300	4	Retain
1282	Gum	10	25	300	4	Retain
1283	Gum	15	30	500	6	Retain
1284	Native	15	20	600	7	Retain
1286	Gum	15	30	600	7	Retain

Specimen Details						
Tree ID	Tree Type	Spread (m)	Height (m)	DBH (mm)	TPZ (m)	Retention
1288	Gum	10	25	400	5	Retain
1289	Gum	10	25	400	5	Retain
1290	Gum	10	25	400	5	Retain
1291	Gum	10	20	300	4	Retain
1292	Gum	10	30	500	6	Retain
1293	Gum	10	25	300	4	Retain
1294	Gum	5	15	300	4	Retain
1295	Gum	15	25	500	6	Retain
1297	Gum	10	15	500	6	Retain
1298	Gum	10	20	400	5	Retain
1299	Gum	10	20	300	4	Retain
1300	Gum	10	30	500	6	Retain
1303	Gum	15	30	500	6	Retain
1304	Gum	10	20	300	4	Retain
1305	Gum	10	20	300	4	Retain
1306	Gum	5	15	300	4	Retain
1307	Gum	10	25	400	5	Retain
1308	Gum	10	25	300	4	Retain
1309	Gum	5	15	300	4	Retain
1310	Gum	10	20	400	5	Retain
1311	Gum	10	20	300	4	Retain
1312	Gum	10	20	400	5	Retain
1313	Gum	15	30	700	8	Retain
1315	Gum	5	20	300	4	Retain
1316	Gum	15	30	500	6	Retain
1317	Gum	10	25	400	5	Retain
1318	Gum	10	30	400	5	Retain
1319	Gum	15	30	500	6	Retain
1320	Gum	15	30	500	6	Retain
1321	Gum	15	30	500	6	Retain

Specimen Details						
Tree ID	Tree Type	Spread (m)	Height (m)	DBH (mm)	TPZ (m)	Retention
1322	Gum	5	20	400	5	Retain
1323	Gum	5	25	400	5	Retain
1324	Gum	10	20	400	5	Retain
1325	Gum	15	30	500	6	Retain
1326	Gum	10	20	400	5	Retain
1327	Gum	10	30	500	6	Retain
1328	Gum	15	30	500	6	Retain
1329	Gum	10	25	400	5	Retain
1330	Gum	5	20	300	4	Retain
1331	Gum	10	25	600	7	Retain
1332	Gum	15	30	500	6	Retain
1333	Gum	10	30	300	4	Retain
1334	Gum	15	30	500	6	Retain
1335	Gum	10	30	500	6	Retain
1336	Gum	10	30	400	5	Retain
1337	Gum	10	30	500	6	Retain
1338	Gum	10	30	500	6	Retain
1339	Gum	5	15	300	4	Retain
1340	Gum	15	25	500	6	Retain
1343	Gum	10	30	500	6	Retain
1344	Gum	10	20	300	4	Retain
1346	Gum	10	20	400	5	Retain
1347	Gum	15	30	500	6	Retain
1348	Gum	15	30	500	6	Retain
1350	Gum	10	30	400	5	Retain
1351	Gum	15	30	500	6	Retain
1352	Gum	10	20	400	5	Remove
1353	Gum	5	20	300	4	Remove
1355	Gum	10	20	400	5	Retain
1357	Native	5	15	300	4	Remove

Specimen Details						
Tree ID	Tree Type	Spread (m)	Height (m)	DBH (mm)	TPZ (m)	Retention
1358	Gum	15	30	800	10	Remove
1359	Gum	15	30	500	6	Remove
1360	Gum	10	25	400	5	Remove
1361	Gum	10	25	400	5	Remove
1363	Gum	5	20	400	5	Remove
1364	Gum	15	30	500	6	Remove
1365	Gum	10	20	400	5	Remove
1367	Gum	10	20	500	6	Remove
1368	Gum	10	25	500	6	Retain
1370	Gum	15	30	500	6	Retain
1371	Gum	15	30	500	6	Retain
1373	Gum	10	30	600	7	Retain
1374	Gum	15	30	600	7	Retain
1376	Gum	15	30	500	6	Retain
1377	Gum	5	20	300	4	Retain
1378	Gum	10	25	400	5	Retain
1379	Gum	5	20	300	4	Retain
1380	Gum	15	30	600	7	Retain
1381	Gum	5	20	300	4	Retain
1382	Gum	5	20	300	4	Retain
1383	Gum	5	20	300	4	Retain
1384	Gum	10	25	400	5	Retain
1385	Gum	10	25	400	5	Retain
1386	Gum	15	30	600	7	Retain
1388	Gum	5	20	500	6	Retain
1389	Gum	10	30	500	6	Retain
1390	Gum	10	20	300	4	Remove
1392	Gum	10	25	300	4	Remove
1393	Gum	10	30	400	5	Remove
1397	Gum	10	25	400	5	Remove

Specimen Details						
Tree ID	Tree Type	Spread (m)	Height (m)	DBH (mm)	TPZ (m)	Retention
1398	Gum	10	25	300	4	Remove
1399	Gum	10	25	300	4	Remove
1400	Gum	10	25	300	4	Remove
1401	Gum	5	20	400	5	Retain
1402	Gum	10	25	500	6	Retain
1404	Gum	15	30	600	7	Retain
1405	Gum	15	30	500	6	Retain
1406	Gum	10	20	500	6	Retain
1407	Gum	5	15	300	4	Retain
1408	Gum	5	20	400	5	Retain
1409	Gum	10	25	300	4	Retain
1412	Gum	15	30	600	7	Retain
1413	Gum	10	20	400	5	Retain
1415	Gum	15	30	600	7	Retain
1416	Gum	15	30	600	7	Retain
1417	Gum	10	15	300	4	Retain
1420	Gum	10	30	500	6	Retain
1421	Gum	10	30	500	6	Retain
1422	Gum	10	25	500	6	Retain
1424	Gum	10	25	300	4	Retain
1425	Gum	10	25	400	5	Retain
1427	Gum	10	25	300	4	Retain
1428	Gum	10	25	400	5	Retain
1429	Gum	10	25	300	4	Retain
1430	Gum	15	30	600	7	Retain
1431	Gum	10	20	300	4	Retain
1432	Gum	10	20	300	4	Retain
1434	Gum	10	30	500	6	Retain
1435	Gum	10	25	300	4	Retain
1436	Gum	15	30	600	7	Retain

Specimen Details						
Tree ID	Tree Type	Spread (m)	Height (m)	DBH (mm)	TPZ (m)	Retention
1437	Gum	15	30	500	6	Retain
1438	Gum	15	30	500	6	Retain
1439	Gum	10	20	400	5	Retain
1440	Gum	10	25	300	4	Retain
1441	Gum	10	25	500	6	Retain
1442	Gum	10	25	400	5	Retain
1443	Gum	15	30	500	6	Retain
1444	Gum	15	30	700	8	Retain
1445	Gum	10	25	300	4	Retain
1446	Gum	10	25	300	4	Retain
1447	Gum	10	25	300	4	Remove
1449	Gum	10	25	300	4	Remove
1450	Gum	15	30	600	7	Remove
1453	Gum	15	30	400	5	Remove
1455	Gum	5	20	300	4	Remove
1456	Native	5	10	400	5	Remove
1457	Gum	15	30	600	7	Remove
1458	Gum	10	25	300	4	Remove
1459	Gum	15	30	600	7	Remove
1460	Gum	15	30	500	6	Remove
1461	Gum	15	30	600	7	Remove
1462	Gum	15	30	700	8	Remove
1463	Gum	15	30	600	7	Remove
1464	Gum	15	25	500	6	Remove
1465	Gum	15	25	400	5	Remove
1466	Gum	15	25	400	5	Remove
1467	Gum	10	25	300	4	Remove
1468	Gum	10	25	300	4	Remove
1469	Gum	10	25	300	4	Remove
1470	Gum	10	25	300	4	Remove

Specimen Details						
Tree ID	Tree Type	Spread (m)	Height (m)	DBH (mm)	TPZ (m)	Retention
1471	Gum	10	25	300	4	Remove
1473	Gum	10	25	300	4	Retain
1474	Gum	10	25	300	4	Retain
1475	Gum	10	30	600	7	Retain
1476	Gum	10	25	300	4	Retain
1477	Gum	10	25	300	4	Retain
1478	Gum	15	30	600	7	Retain
1480	Gum	15	30	500	6	Retain
1481	Gum	5	20	300	4	Retain
1482	Gum	15	30	600	7	Retain
1483	Gum	5	20	300	4	Retain
1486	Gum	15	30	600	7	Retain
1487	Gum	15	30	500	6	Retain
1488	Gum	15	25	400	5	Retain
1489	Gum	15	25	500	6	Retain
1491	Gum	15	20	400	5	Retain
1492	Gum	10	20	400	5	Remove
1493	Gum	10	25	300	4	Retain
1494	Gum	10	25	400	5	Retain
1495	Gum	10	25	300	4	Retain
1496	Gum	10	20	300	4	Retain
1497	Gum	10	20	400	5	Retain
1498	Gum	10	20	300	4	Retain
1499	Gum	10	10	400	5	Retain
1500	Gum	15	30	500	6	Retain
1501	Gum	10	25	300	4	Retain
1502	Gum	10	25	400	5	Retain
1504	Gum	10	25	500	6	Retain
1505	Gum	15	30	600	7	Retain
1506	Gum	10	25	400	5	Retain

Specimen Details						
Tree ID	Tree Type	Spread (m)	Height (m)	DBH (mm)	TPZ (m)	Retention
1507	Gum	5	20	500	6	Retain
1508	Gum	15	30	600	7	Retain
1509	Gum	10	20	300	4	Retain
1510	Gum	10	25	400	5	Retain
1511	Gum	15	30	700	8	Retain
1512	Gum	10	30	400	5	Retain
1513	Gum	10	30	400	5	Retain
1514	Gum	15	30	600	7	Retain
1515	Gum	10	30	500	6	Retain
1517	Gum	10	25	400	5	Retain
1518	Gum	10	30	500	6	Retain
1519	Gum	10	30	400	5	Retain
1520	Gum	15	30	600	7	Retain
1521	Gum	10	30	400	5	Retain
1522	Gum	10	30	400	5	Retain
1523	Gum	15	30	600	7	Retain
1524	Gum	15	25	400	5	Retain
1525	Paperbark	3	10	300	4	Retain
1526	Gum	15	30	500	6	Retain
1527	Gum	10	30	500	6	Retain
1528	Gum	10	30	500	6	Retain
1529	Gum	15	30	600	7	Retain
1531	Gum	10	25	400	5	Retain
1532	Gum	10	25	500	6	Retain
1533	Gum	5	25	300	4	Retain
1534	Gum	5	15	300	4	Retain
1535	Gum	10	30	600	7	Retain
1536	Gum	10	25	400	5	Remove
1537	Gum	10	25	400	5	Retain
1538	Native	15	20	300	4	Remove

Specimen Details						
Tree ID	Tree Type	Spread (m)	Height (m)	DBH (mm)	TPZ (m)	Retention
1539	Gum	10	25	700	8	Remove
1540	Gum	10	25	300	4	Retain
1541	Gum	10	20	300	4	Retain
1543	Gum	10	15	500	6	Retain
1544	Gum	10	20	400	5	Retain
1545	Gum	10	30	700	8	Retain
1546	Gum	10	25	400	5	Retain
1548	Gum	10	25	500	6	Retain
1549	Gum	5	10	400	5	Retain
1551	Gum	10	20	400	5	Retain
1554	Gum	10	20	300	4	Retain
1555	Gum	10	15	300	4	Retain
1556	Gum	10	20	300	4	Retain
1557	Gum	10	25	500	6	Retain
1558	Gum	10	20	300	4	Retain
1559	Gum	10	15	300	4	Remove
1560	Gum	10	15	400	5	Remove
1561	Gum	10	15	300	4	Remove
1562	Gum	10	15	300	4	Remove
1563	Gum	10	15	300	4	Remove
1564	Gum	10	15	300	4	Remove
1565	Gum	10	15	300	4	Remove
1566	Gum	10	15	300	4	Remove
1567	Gum	15	15	350	4	Remove
1568	Gum	10	15	300	4	Remove
1569	Gum	10	15	300	4	Remove
1570	Gum	10	15	350	4	Remove
1571	Gum	10	15	300	4	Remove
1572	Gum	10	15	300	4	Remove
1573	Gum	10	15	400	5	Remove

Specimen Details						
Tree ID	Tree Type	Spread (m)	Height (m)	DBH (mm)	TPZ (m)	Retention
1574	Gum	10	15	300	4	Remove
1575	Gum	10	15	350	4	Remove
1576	Gum	10	15	400	5	Remove
1577	Gum	10	15	300	4	Remove
1578	Gum	10	15	300	4	Remove
1579	Gum	10	15	300	4	Remove
1580	Gum	8	20	450	5	Remove
1581	Gum	15	20	600	7	Remove
1582	Gum	10	15	350	4	Remove
1583	Gum	10	15	400	5	Remove
1584	Gum	10	15	350	4	Remove
1585	Gum	10	15	350	4	Remove
1586	Gum	10	15	350	4	Remove
1587	Gum	10	15	300	4	Remove
1588	Gum	10	15	300	4	Remove
1589	Gum	10	15	350	4	Remove
1590	Gum	10	15	500	6	Remove
1591	Gum	10	15	400	5	Remove
1592	Gum	10	15	300	4	Remove
1593	Gum	10	15	450	5	Remove
1594	Gum	10	15	350	4	Remove
1595	Gum	10	15	300	4	Remove
1596	Gum	10	20	300	4	Remove
1597	Gum	10	20	300	4	Remove
1598	Gum	10	20	300	4	Remove
1599	Gum	10	15	300	4	Remove
1600	Gum	20	15	650	8	Remove
1601	Gum	10	15	400	5	Remove
1602	Gum	10	15	300	4	Remove
1603	Gum	10	15	300	4	Remove

Specimen Details						
Tree ID	Tree Type	Spread (m)	Height (m)	DBH (mm)	TPZ (m)	Retention
1604	Gum	10	15	400	5	Remove
1605	Gum	10	15	300	4	Remove
1606	Gum	10	15	500	6	Remove
1607	Gum	10	15	400	5	Remove
1608	Gum	10	15	300	4	Remove
1609	Paperbark	10	15	300	4	Remove
1610	Gum	10	15	300	4	Remove
1611	Gum	10	15	300	4	Remove
1612	Gum	10	15	300	4	Remove
1613	Gum	10	15	400	5	Remove
1614	Gum	10	15	350	4	Remove
1615	Gum	10	15	500	6	Remove
1616	Gum	10	15	400	5	Remove
1617	Gum	15	15	500	6	Remove
1618	Gum	10	15	300	4	Remove
1619	Gum	10	15	300	4	Remove
1620	Gum	10	15	350	4	Remove
1621	Gum	15	15	500	6	Remove
1622	Gum	10	15	350	4	Remove
1623	Gum	10	15	300	4	Remove
1624	Gum	10	15	400	5	Remove
1625	Gum	10	15	350	4	Remove
1626	Gum	20	15	450	5	Remove
1627	Gum	10	15	300	4	Remove
1628	Gum	10	15	400	5	Remove
1629	Gum	10	15	300	4	Remove
1630	Gum	10	15	300	4	Remove
1631	Gum	10	15	400	5	Remove
1632	Gum	10	15	350	4	Remove
1633	Gum	10	15	350	4	Remove

Specimen Details						
Tree ID	Tree Type	Spread (m)	Height (m)	DBH (mm)	TPZ (m)	Retention
1634	Gum	10	15	300	4	Remove
1635	Paperbark	10	15	300	4	Remove
1636	Paperbark	10	15	300	4	Remove
1637	Gum	10	15	300	4	Remove
1638	Gum	10	15	300	4	Remove
1639	Gum	10	15	300	4	Remove
1640	Gum	10	15	350	4	Remove
1641	Gum	10	15	350	4	Remove
1642	Gum	10	15	350	4	Remove
1643	Gum	15	20	500	6	Remove
1644	Gum	10	15	400	5	Remove
1645	Gum	10	15	350	4	Remove
1646	Gum	10	15	350	4	Remove
1647	Gum	10	15	300	4	Remove
1648	Gum	10	15	300	4	Remove
1649	Gum	10	15	300	4	Remove
1650	Gum	10	15	400	5	Remove
1651	Gum	10	15	300	4	Remove
1652	Paperbark	10	15	300	4	Remove
1653	Gum	10	15	300	4	Remove
1654	Gum	10	15	300	4	Remove
1655	Gum	10	15	350	4	Remove
1656	Gum	10	15	300	4	Remove
1657	Gum	10	15	300	4	Remove
1658	Gum	10	15	400	5	Remove
1659	Gum	10	15	400	5	Remove
1660	Gum	10	15	350	4	Remove
1662	Gum	10	15	300	4	Remove
1663	Gum	10	15	400	5	Remove
1664	Gum	10	15	300	4	Remove

Specimen Details						
Tree ID	Tree Type	Spread (m)	Height (m)	DBH (mm)	TPZ (m)	Retention
1665	Gum	10	15	450	5	Remove
1666	Paperbark	10	15	300	4	Remove
1667	Paperbark	5	15	300	4	Remove
1668	Gum	10	15	350	4	Remove
1669	Gum	15	15	550	7	Remove
1670	Gum	10	15	350	4	Remove
1671	Gum	10	15	500	6	Remove
1672	Gum	10	15	300	4	Remove
1673	Gum	15	15	400	5	Remove
1674	Gum	10	15	300	4	Remove
1676	Gum	10	15	400	5	Remove
1677	Gum	10	15	300	4	Remove
1678	Gum	10	15	300	4	Remove
1679	Gum	10	15	350	4	Remove
1680	Gum	10	15	300	4	Remove
1681	Gum	10	15	400	5	Remove
1682	Gum	10	15	300	4	Remove
1683	Paperbark	10	15	300	4	Remove
1684	Paperbark	10	15	300	4	Remove
1685	Paperbark	10	15	300	4	Remove
1686	Gum	10	15	400	5	Remove
1687	Gum	10	15	300	4	Remove
1688	Gum	10	20	300	4	Remove
1689	Gum	10	15	500	6	Remove
1690	Paperbark	10	15	300	4	Remove
1691	Gum	10	15	450	5	Remove
1692	Gum	10	15	400	5	Remove
1693	Gum	10	15	400	5	Remove
1694	Gum	10	15	350	4	Remove
1695	Gum	10	15	300	4	Remove

Specimen Details						
Tree ID	Tree Type	Spread (m)	Height (m)	DBH (mm)	TPZ (m)	Retention
1696	Gum	10	15	450	5	Remove
1697	Gum	15	20	400	5	Remove
1698	Gum	10	15	300	4	Remove
1699	Paperbark	10	15	300	4	Remove
1700	Gum	10	15	300	4	Remove
1701	Paperbark	10	15	300	4	Remove
1702	Gum	15	20	1000	12	Remove
1703	Gum	10	15	300	4	Remove
1704	Gum	10	15	350	4	Remove
1705	Gum	10	15	400	5	Remove
1706	Gum	10	15	400	5	Remove
1707	Gum	10	15	500	6	Remove
1708	Gum	10	20	600	7	Remove
1709	Gum	10	15	500	6	Remove
1710	Gum	10	15	400	5	Remove
1711	Gum	5	15	500	6	Retain
1712	Gum	5	15	500	6	Retain
1713	Gum	5	15	500	6	Retain
1714	Gum	10	25	500	6	Retain
1715	Gum	15	25	600	7	Retain
1716	Gum	10	25	300	4	Retain
1717	Gum	10	20	300	4	Retain
1718	Gum	10	25	400	5	Remove
1719	Gum	10	20	300	4	Remove
1720	Gum	10	20	300	4	Retain
1721	Gum	10	25	400	5	Retain
1722	Gum	5	15	400	5	Retain
1723	Gum	5	20	300	4	Remove
1724	Gum	10	20	500	6	Retain
1725	Gum	10	20	500	6	Retain

Specimen Details						
Tree ID	Tree Type	Spread (m)	Height (m)	DBH (mm)	TPZ (m)	Retention
1729	Gum	5	25	300	4	Retain
1730	Gum	5	20	300	4	Retain
1731	Gum	5	20	300	4	Remove
1732	Gum	10	30	500	6	Retain
1733	Gum	10	30	500	6	Retain
1735	Gum	10	25	500	6	Retain
1736	Gum	10	25	400	5	Retain
1739	Gum	10	25	600	7	Retain
1740	Gum	10	20	300	4	Remove
1741	Gum	10	20	300	4	Retain
1742	Gum	10	20	300	4	Remove
1743	Gum	10	20	300	4	Remove
1744	Gum	10	25	300	4	Retain
1745	Gum	10	20	300	4	Retain
1746	Gum	10	25	300	4	Remove
1747	Gum	15	25	500	6	Retain
1748	Gum	15	30	500	6	Retain
1750	Gum	10	25	500	6	Retain
1751	Gum	10	25	400	5	Retain
1752	Gum	10	25	400	5	Retain
1753	Paperbark	5	15	300	4	Retain
1754	Gum	10	30	450	5	Retain
1755	Gum	10	25	300	4	Retain
1758	Paperbark	10	10	300	4	Retain
1759	Gum	10	25	400	5	Retain
1760	Gum	10	25	300	4	Retain
1761	Gum	15	25	500	6	Retain
1762	Gum	15	30	500	6	Retain
1763	Gum	15	25	500	6	Retain
1764	Gum	15	25	700	8	Retain

Specimen Details						
Tree ID	Tree Type	Spread (m)	Height (m)	DBH (mm)	TPZ (m)	Retention
1766	Gum	10	20	300	4	Retain
1768	Gum	10	20	300	4	Retain
1769	Gum	15	30	600	7	Retain
1770	Gum	15	25	700	8	Retain
1771	Gum	10	25	400	5	Retain
1773	Gum	15	30	600	7	Retain
1777	Native	5	15	300	4	Retain
1778	Gum	15	30	600	7	Retain
1779	Gum	10	20	400	5	Retain
1780	Gum	10	20	400	5	Retain
1781	Gum	10	25	500	6	Retain
1782	Native	5	15	300	4	Retain
1783	Gum	15	30	600	7	Retain
1784	Gum	5	15	400	5	Retain
1786	Gum	10	20	400	5	Retain
1787	Gum	10	20	400	5	Retain
1788	Gum	10	20	400	5	Retain
1789	Gum	10	20	400	5	Retain
1790	Gum	10	20	600	7	Retain
1791	Gum	10	25	600	7	Retain
1792	Gum	15	30	600	7	Retain
1793	Paperbark	5	15	300	4	Retain
1794	Paperbark	5	15	300	4	Retain
1795	Gum	5	15	300	4	Retain
1796	Gum	15	30	400	5	Retain
1797	Gum	15	30	500	6	Retain
1798	Gum	15	30	500	6	Retain
1799	Gum	15	30	500	6	Retain
1802	Gum	10	25	500	6	Retain
1803	Gum	15	30	500	6	Retain

Specimen Details						
Tree ID	Tree Type	Spread (m)	Height (m)	DBH (mm)	TPZ (m)	Retention
1807	Gum	10	20	400	5	Remove
1808	Gum	10	25	400	5	Retain
1809	Gum	15	30	500	6	Retain
1812	Gum	10	25	400	5	Retain
1813	Gum	10	25	500	6	Retain
1814	Gum	10	25	400	5	Retain
1815	Gum	10	20	300	4	Retain
1816	Gum	15	25	500	6	Retain
1817	Gum	10	20	300	4	Retain
1818	Gum	10	25	300	4	Retain
1819	Gum	10	20	300	4	Retain
1820	Gum	5	15	300	4	Retain
1821	Gum	5	15	300	4	Retain
1822	Gum	15	30	500	6	Retain
1823	Paperbark	5	15	300	4	Retain
1824	Paperbark	10	20	500	6	Retain
1826	Gum	5	20	400	5	Retain
1827	Gum	10	20	400	5	Retain
1829	Gum	15	25	700	8	Retain
1830	Gum	15	25	500	6	Retain
1831	Gum	15	25	500	6	Retain
1832	Gum	10	20	400	5	Retain
1833	Gum	10	20	400	5	Retain
1834	Gum	10	25	400	5	Retain
1835	Gum	10	25	400	5	Retain
1837	Gum	10	25	400	5	Retain
1838	Paperbark	5	10	300	4	Retain
1839	Paperbark	5	15	300	4	Retain
1840	Gum	10	30	400	5	Retain
1841	Gum	15	30	600	7	Retain

Specimen Details						
Tree ID	Tree Type	Spread (m)	Height (m)	DBH (mm)	TPZ (m)	Retention
1842	Paperbark	5	15	300	4	Retain
1843	Gum	15	30	500	6	Retain
1844	Gum	15	25	400	5	Retain
1845	Paperbark	5	15	300	4	Retain
1846	Gum	15	30	600	7	Retain
1847	Gum	15	25	500	6	Retain
1848	Gum	10	20	300	4	Retain
1849	Gum	15	25	500	6	Retain
1850	Gum	10	20	400	5	Retain
1851	Gum	15	30	600	7	Retain
1855	Gum	10	25	500	6	Retain
1856	Gum	15	30	600	7	Retain
1857	Paperbark	5	15	300	4	Retain
1859	Gum	15	30	500	6	Retain
1860	Gum	10	25	400	5	Retain
1861	Gum	10	20	400	5	Retain
1862	Gum	10	20	300	4	Retain
1863	Gum	10	20	300	4	Retain
1864	Gum	10	20	300	4	Retain
1865	Gum	10	25	500	6	Retain
1866	Gum	10	25	400	5	Retain
1867	Gum	10	20	400	5	Retain
1868	Gum	10	20	400	5	Retain
1869	Gum	5	20	400	5	Retain
1870	Gum	10	25	500	6	Retain
1871	Gum	10	20	300	4	Retain
1872	Gum	10	30	500	6	Retain
1873	Gum	10	10	300	4	Retain
1874	Gum	10	20	400	5	Retain
1875	Gum	10	25	500	6	Retain

Specimen Details						
Tree ID	Tree Type	Spread (m)	Height (m)	DBH (mm)	TPZ (m)	Retention
1876	Gum	10	25	400	5	Retain
1877	Gum	10	20	400	5	Retain
1878	Gum	10	20	300	4	Retain
1880	Gum	10	20	400	5	Retain
1881	Paperbark	5	10	300	4	Retain
1882	Gum	10	25	500	6	Retain
1885	Gum	10	20	450	5	Retain
1886	Gum	10	20	400	5	Retain
1888	Gum	5	20	500	6	Retain
1889	Gum	10	30	450	5	Retain
1890	Gum	15	25	400	5	Retain
1891	Gum	5	20	400	5	Retain
1892	Paperbark	5	10	300	4	Retain
1893	Gum	15	25	500	6	Retain
1895	Gum	10	20	400	5	Retain
1896	Gum	15	30	600	7	Retain
1897	Gum	10	25	600	7	Remove
1901	Gum	10	25	400	5	Retain
1902	Gum	10	25	400	5	Retain
1904	Gum	10	25	500	6	Retain
1905	Gum	5	25	300	4	Retain
1906	Gum	10	25	400	5	Retain
1907	Gum	5	20	300	4	Retain
1908	Gum	15	25	500	6	Retain
1910	Gum	5	20	400	5	Retain
1911	Gum	5	25	500	6	Retain
1912	Gum	5	20	300	4	Retain
1913	Gum	10	25	500	6	Retain
1914	Gum	10	25	500	6	Retain
1915	Gum	10	20	400	5	Retain

Specimen Details						
Tree ID	Tree Type	Spread (m)	Height (m)	DBH (mm)	TPZ (m)	Retention
1916	Gum	10	20	400	5	Retain
1919	Gum	15	30	600	7	Retain
1920	Gum	5	25	600	7	Retain
1923	Gum	10	20	300	4	Retain
1925	Gum	10	20	300	4	Retain
1926	Gum	10	20	300	4	Retain
1927	Gum	10	20	400	5	Retain
1928	Gum	10	25	500	6	Retain
1929	Gum	15	25	600	7	Retain
1930	Gum	10	25	500	6	Retain
1931	Gum	10	20	300	4	Retain
1932	Gum	10	20	400	5	Retain
1933	Gum	10	20	400	5	Retain
1934	Gum	10	25	500	6	Retain
1935	Gum	10	25	500	6	Retain
1936	Gum	10	25	400	5	Retain
1937	Gum	10	25	400	5	Retain
1938	Gum	10	25	400	5	Retain
1940	Gum	10	25	400	5	Remove
1941	Gum	15	25	400	5	Retain
1942	Gum	5	25	300	4	Retain
1943	Gum	10	25	400	5	Retain
1944	Gum	15	25	500	6	Retain
1945	Gum	10	25	500	6	Retain
1946	Gum	10	20	300	4	Retain
1947	Gum	5	20	300	4	Retain
1948	Gum	5	20	400	5	Retain
1949	Gum	5	20	300	4	Retain
1950	Gum	5	20	300	4	Retain
1951	Gum	5	20	300	4	Retain

Specimen Details						
Tree ID	Tree Type	Spread (m)	Height (m)	DBH (mm)	TPZ (m)	Retention
1952	Gum	5	20	300	4	Retain
1953	Gum	10	20	400	5	Retain
1954	Gum	10	25	500	6	Retain
1955	Gum	10	20	300	4	Retain
1956	Gum	10	20	300	4	Retain
1957	Gum	10	25	400	5	Retain
1958	Gum	5	20	300	4	Retain
1959	Gum	5	20	300	4	Retain
1960	Gum	10	20	300	4	Retain
1961	Gum	10	25	500	6	Retain
1962	Gum	5	20	300	4	Retain
1964	Gum	10	25	400	5	Retain
1965	Gum	15	20	400	5	Retain
1966	Gum	10	25	400	5	Retain
1967	Gum	10	25	400	5	Retain
1968	Gum	10	20	400	5	Retain
1969	Gum	15	25	450	5	Retain
1970	Gum	5	20	300	4	Retain
1971	Gum	10	20	400	5	Retain
1972	Gum	10	25	450	5	Retain
1973	Paperbark	5	15	300	4	Retain
1974	Gum	5	20	450	5	Retain
1975	Gum	5	15	300	4	Remove
1976	Gum	10	25	400	5	Retain
1977	Gum	10	25	400	5	Retain
1978	Gum	10	20	400	5	Retain
1979	Gum	10	30	700	8	Retain
1980	Gum	15	30	600	7	Retain
1981	Gum	5	20	400	5	Retain
1982	Gum	15	30	500	6	Retain

Specimen Details						
Tree ID	Tree Type	Spread (m)	Height (m)	DBH (mm)	TPZ (m)	Retention
1983	Gum	10	20	300	4	Retain
1984	Gum	10	20	400	5	Retain
1985	Gum	10	20	400	5	Retain
1986	Gum	10	25	400	5	Retain
1987	Gum	5	15	400	5	Retain
1988	Gum	5	15	300	4	Retain
1989	Gum	10	25	400	5	Retain
1990	Gum	10	25	500	6	Retain
1991	Gum	10	25	400	5	Retain
1992	Gum	10	30	500	6	Retain
1994	Gum	10	20	300	4	Retain
1995	Gum	15	25	600	7	Retain
1996	Gum	10	20	300	4	Retain
1997	Gum	10	20	400	5	Retain
1998	Gum	5	20	400	5	Retain
1999	Gum	10	20	300	4	Retain
2000	Gum	10	20	300	4	Retain
2001	Gum	10	20	400	5	Retain
2002	Gum	10	20	400	5	Retain
2003	Gum	5	15	400	5	Retain
2004	Gum	10	20	300	4	Retain
2005	Paperbark	5	15	300	4	Retain
2006	Gum	10	30	500	6	Retain
2008	Gum	10	20	400	5	Retain
2009	Gum	10	20	400	5	Retain
2010	Gum	15	25	500	6	Retain
2012	Gum	5	15	300	4	Retain
2013	Gum	10	20	400	5	Retain
2014	Gum	10	20	300	4	Retain
2016	Gum	10	25	900	11	Retain

Specimen Details						
Tree ID	Tree Type	Spread (m)	Height (m)	DBH (mm)	TPZ (m)	Retention
2017	Gum	10	20	300	4	Retain
2018	Gum	10	20	300	4	Retain
2019	Gum	10	20	400	5	Retain
2020	Gum	10	25	400	5	Retain
2021	Gum	5	20	300	4	Retain
2022	Gum	5	20	400	5	Retain
2023	Gum	5	15	400	5	Retain
2024	Gum	10	20	400	5	Retain
2025	Gum	15	30	500	6	Retain
2026	Gum	10	15	500	6	Retain
2027	Gum	10	20	400	5	Retain
2028	Gum	10	20	350	4	Retain
2029	Gum	5	15	350	4	Retain
2030	Gum	10	20	400	5	Retain
2031	Gum	10	20	300	4	Retain
2032	Gum	15	20	600	7	Retain
2033	Gum	5	15	300	4	Retain
2034	Gum	5	15	300	4	Retain
2035	Gum	10	25	500	6	Retain
2036	Gum	10	20	400	5	Retain
2037	Gum	10	20	400	5	Retain
2038	Gum	5	15	300	4	Retain
2039	Gum	10	25	400	5	Retain
2040	Gum	10	25	400	5	Retain
2041	Gum	10	30	500	6	Retain
2042	Gum	10	20	400	5	Retain
2043	Gum	10	20	400	5	Retain
2044	Gum	5	15	300	4	Retain
2045	Gum	5	15	300	4	Retain
2046	Gum	10	30	500	6	Retain

Specimen Details						
Tree ID	Tree Type	Spread (m)	Height (m)	DBH (mm)	TPZ (m)	Retention
2048	Gum	15	20	400	5	Retain
2049	Gum	5	15	400	5	Retain
2050	Gum	10	20	400	5	Retain
2051	Gum	10	20	400	5	Retain
2052	Gum	10	25	400	5	Retain
2053	Gum	10	20	400	5	Retain
2054	Gum	5	15	300	4	Retain
2055	Gum	5	20	400	5	Retain
2056	Gum	5	15	300	4	Retain
2057	Gum	5	15	300	4	Retain
2058	Gum	15	30	700	8	Retain
2059	Gum	10	20	400	5	Retain
2060	Gum	10	20	300	4	Retain
2061	Gum	10	20	400	5	Retain
2062	Gum	5	15	400	5	Retain
2063	Gum	5	20	450	5	Retain
2064	Gum	5	10	300	4	Retain
2065	Gum	5	15	300	4	Retain
2066	Gum	10	20	400	5	Retain
2067	Gum	10	25	500	6	Retain
2069	Gum	5	15	300	4	Retain
2070	Gum	5	15	300	4	Retain
2071	Gum	10	20	450	5	Retain
2072	Gum	10	25	400	5	Retain
2073	Gum	10	25	400	5	Retain
2074	Gum	10	25	400	5	Retain
2075	Gum	5	20	300	4	Retain
2076	Gum	10	25	500	6	Retain
2077	Gum	10	20	300	4	Retain
2078	Gum	10	20	300	4	Retain

Specimen Details						
Tree ID	Tree Type	Spread (m)	Height (m)	DBH (mm)	TPZ (m)	Retention
2079	Gum	10	20	300	4	Retain
2080	Gum	10	25	400	5	Retain
2081	Gum	10	20	400	5	Retain
2085	Gum	5	15	300	4	Remove
2086	Gum	15	30	500	6	Retain
2088	Gum	5	20	400	5	Retain
2089	Gum	5	25	450	5	Retain
2090	Gum	5	15	300	4	Retain
2092	Gum	15	25	450	5	Retain
2093	Gum	10	30	450	5	Retain
2094	Gum	10	25	400	5	Remove
2096	Gum	5	15	300	4	Remove
2097	Gum	10	25	500	6	Retain
2098	Gum	10	20	400	5	Retain
2100	Gum	5	15	300	4	Retain
2101	Gum	5	15	300	4	Retain
2102	Gum	5	15	300	4	Retain
2103	Gum	10	25	450	5	Retain
2104	Gum	10	25	400	5	Retain
2105	Gum	10	25	400	5	Retain
2106	Gum	10	25	400	5	Retain
2107	Gum	10	25	400	5	Retain
2108	Gum	10	10	300	4	Retain
2109	Gum	5	15	400	5	Retain
2111	Gum	5	20	300	4	Retain
2112	Gum	5	20	300	4	Retain
2114	Gum	10	20	300	4	Retain
2115	Gum	10	20	300	4	Retain
2116	Gum	10	25	450	5	Retain
2117	Gum	10	25	500	6	Retain

Specimen Details						
Tree ID	Tree Type	Spread (m)	Height (m)	DBH (mm)	TPZ (m)	Retention
2118	Gum	10	30	500	6	Retain
2120	Gum	10	20	450	5	Retain
2121	Gum	10	20	450	5	Retain
2122	Gum	5	15	300	4	Retain
2123	Gum	15	30	500	6	Retain
2124	Gum	10	20	300	4	Retain
2125	Gum	10	25	450	5	Retain
2126	Gum	15	25	450	5	Retain
2127	Gum	10	25	400	5	Retain
2128	Gum	10	25	500	6	Retain
2129	Gum	10	25	400	5	Retain
2130	Gum	10	20	400	5	Retain
2131	Gum	10	20	400	5	Retain
2132	Gum	10	20	400	5	Retain
2133	Gum	5	25	400	5	Retain
2134	Gum	5	20	300	4	Retain
2135	Gum	5	20	300	4	Retain
2136	Gum	10	25	400	5	Retain
2138	Gum	10	20	400	5	Retain
2139	Gum	10	20	300	4	Retain
2140	Gum	10	20	400	5	Retain
2141	Gum	10	20	400	5	Retain
2142	Gum	10	20	300	4	Retain
2143	Gum	5	25	300	4	Retain
2144	Gum	5	25	300	4	Retain
2145	Gum	10	25	500	6	Retain
2146	Gum	5	20	400	5	Retain
2148	Gum	10	25	400	5	Retain
2149	Gum	10	25	400	5	Retain
2150	Gum	10	30	600	7	Retain

Specimen Details						
Tree ID	Tree Type	Spread (m)	Height (m)	DBH (mm)	TPZ (m)	Retention
2151	Gum	10	30	500	6	Retain
2152	Gum	10	25	400	5	Retain
2153	Gum	5	15	300	4	Retain
2154	Gum	10	25	400	5	Retain
2155	Gum	5	15	300	4	Retain
2156	Gum	10	25	500	6	Retain
2157	Gum	10	20	300	4	Retain
2158	Gum	10	20	400	5	Retain
2159	Gum	10	25	400	5	Retain
2160	Gum	10	25	400	5	Retain
2161	Gum	15	30	500	6	Retain
2162	Gum	10	20	400	5	Retain
2163	Gum	10	20	400	5	Retain
2164	Gum	10	20	300	4	Retain
2165	Gum	15	30	600	7	Retain
2166	Gum	15	30	600	7	Retain
2169	Gum	15	30	600	7	Retain
2170	Gum	15	30	500	6	Retain
2171	Gum	10	25	400	5	Retain
2172	Gum	15	30	600	7	Retain
2173	Gum	10	20	400	5	Retain
2174	Gum	10	20	400	5	Retain
2176	Gum	15	30	600	7	Retain
2178	Gum	10	25	400	5	Retain
2179	Gum	5	20	400	5	Retain
2180	Gum	10	20	300	4	Retain
2181	Gum	10	25	500	6	Retain
2182	Native	5	10	300	4	Retain
2183	Gum	5	15	300	4	Retain
2184	Gum	10	25	400	5	Retain

Specimen Details						
Tree ID	Tree Type	Spread (m)	Height (m)	DBH (mm)	TPZ (m)	Retention
2185	Gum	5	15	300	4	Retain
2186	Gum	15	30	500	6	Retain
2187	Gum	5	20	300	4	Retain
2188	Gum	10	25	500	6	Retain
2189	Gum	15	30	700	8	Retain
2190	Gum	15	30	500	6	Retain
2191	Gum	10	25	400	5	Retain
2192	Gum	10	25	400	5	Retain
2195	Gum	15	30	500	6	Retain
2196	Gum	10	25	500	6	Retain
2197	Gum	15	30	500	6	Retain
2198	Gum	10	20	500	6	Retain
2200	Gum	15	30	600	7	Retain
2202	Gum	15	30	600	7	Retain
2203	Gum	10	25	500	6	Retain
2204	Gum	10	20	500	6	Retain
2205	Gum	10	20	400	5	Retain
2206	Gum	10	20	400	5	Retain
2207	Gum	20	30	800	10	Retain
2208	Gum	10	25	500	6	Retain
2209	Gum	10	25	400	5	Retain
2210	Gum	10	20	400	5	Retain
2211	Gum	15	30	600	7	Retain
2212	Gum	15	25	500	6	Retain
2213	Gum	5	15	300	4	Retain
2214	Gum	10	20	400	5	Retain
2215	Gum	10	20	400	5	Retain
2216	Gum	10	20	400	5	Retain
2217	Gum	10	25	300	4	Retain
2218	Gum	10	20	400	5	Retain

Specimen Details						
Tree ID	Tree Type	Spread (m)	Height (m)	DBH (mm)	TPZ (m)	Retention
2219	Gum	10	30	500	6	Retain
2220	Gum	10	20	300	4	Retain
2221	Gum	10	25	400	5	Retain
2222	Gum	10	25	400	5	Retain
2223	Gum	10	20	400	5	Retain
2224	Gum	10	25	300	4	Retain
2225	Gum	10	25	450	5	Retain
2226	Paperbark	5	15	300	4	Retain
2227	Gum	15	30	500	6	Retain
2229	Gum	10	25	450	5	Retain
2230	Gum	5	15	300	4	Retain
2231	Gum	5	15	300	4	Retain
2232	Gum	5	15	300	4	Retain
2233	Gum	10	25	300	4	Retain
2261	Gum	10	15	300	4	Remove
2262	Gum	10	15	350	4	Remove
2263	Gum	10	15	350	4	Remove
2264	Gum	10	15	300	4	Remove
2265	Gum	10	15	400	5	Remove
2266	Gum	10	15	350	4	Remove
2267	Gum	10	15	300	4	Remove
2268	Gum	15	20	700	8	Remove
2269	Gum	10	15	300	4	Remove
2270	Gum	10	15	400	5	Remove
2271	Gum	10	15	350	4	Remove
2272	Gum	10	15	400	5	Remove
2273	Paperbark	10	15	300	4	Remove
2274	Gum	10	15	300	4	Remove
2275	Gum	15	20	550	7	Remove
2276	Gum	10	15	400	5	Remove

Specimen Details						
Tree ID	Tree Type	Spread (m)	Height (m)	DBH (mm)	TPZ (m)	Retention
2278	Gum	10	15	300	4	Remove
2280	Gum	10	15	350	4	Remove
2281	Gum	10	15	300	4	Remove
2283	Paperbark	10	15	300	4	Remove
2284	Gum	10	15	300	4	Remove
2285	Gum	10	15	300	4	Remove
2286	Gum	10	15	350	4	Remove
2287	Gum	10	15	300	4	Remove
2288	Gum	10	15	300	4	Remove
2289	Gum	10	15	300	4	Remove
2290	Gum	10	15	300	4	Remove
2292	Gum	10	15	550	7	Remove
2293	Gum	10	15	300	4	Remove
2295	Gum	15	20	500	6	Remove
2296	Gum	10	15	350	4	Remove
2297	Gum	10	15	400	5	Remove
2298	Gum	10	15	300	4	Remove
2299	Gum	10	15	300	4	Remove
2300	Paperbark	10	15	300	4	Remove
2301	Gum	10	15	300	4	Remove
2303	Gum	10	15	300	4	Remove
2304	Gum	10	15	300	4	Remove
2305	Gum	10	15	400	5	Remove
2306	Gum	10	15	350	4	Remove
2307	Gum	10	15	350	4	Remove
2308	Gum	10	15	350	4	Remove
2309	Gum	10	15	300	4	Remove
2310	Gum	10	15	400	5	Remove
2311	Gum	10	15	400	5	Remove
2312	Gum	10	15	300	4	Remove

Specimen Details						
Tree ID	Tree Type	Spread (m)	Height (m)	DBH (mm)	TPZ (m)	Retention
2313	Gum	10	15	350	4	Remove
2314	Gum	10	15	350	4	Remove
2315	Gum	10	15	300	4	Remove
2316	Paperbark	10	15	300	4	Remove
2317	Paperbark	10	15	300	4	Remove
2318	Paperbark	10	15	300	4	Remove
2320	Gum	15	15	450	5	Remove
2321	Gum	10	15	300	4	Remove
2322	Gum	15	20	550	7	Remove
2323	Gum	15	20	550	7	Remove
2324	Gum	10	15	300	4	Remove
2326	Gum	10	15	300	4	Remove
2327	Gum	10	15	300	4	Remove
2328	Gum	10	15	400	5	Remove
2329	Gum	15	15	450	5	Remove
2331	Gum	15	15	650	8	Remove
2332	Gum	10	15	450	5	Remove
2334	Gum	10	15	350	4	Remove
2335	Gum	15	20	500	6	Remove
2336	Gum	10	15	300	4	Remove
2337	Gum	10	15	300	4	Remove
2338	Gum	15	20	1000	12	Remove
2339	Gum	10	15	350	4	Remove
2340	Gum	10	15	400	5	Remove
2341	Gum	10	15	300	4	Remove
2342	Gum	10	15	350	4	Remove
2343	Gum	15	15	600	7	Remove
2344	Gum	10	15	350	4	Remove
2345	Gum	10	15	300	4	Remove
2346	Gum	10	15	300	4	Remove

Specimen Details						
Tree ID	Tree Type	Spread (m)	Height (m)	DBH (mm)	TPZ (m)	Retention
2347	Gum	10	15	300	4	Remove
2348	Gum	10	15	350	4	Remove
2349	Paperbark	10	15	350	4	Remove
2350	Gum	10	15	300	4	Remove
2351	Gum	10	15	300	4	Remove
2352	Gum	10	15	350	4	Remove
2353	Gum	10	15	300	4	Remove
2354	Gum	10	15	350	4	Remove
2355	Gum	10	15	350	4	Remove
2356	Gum	10	15	400	5	Remove
2357	Gum	10	20	700	8	Remove
2358	Gum	10	15	350	4	Remove
2359	Gum	10	15	300	4	Remove
2360	Gum	10	15	450	5	Remove
2361	Gum	10	15	450	5	Remove
2362	Gum	10	20	450	5	Remove
2363	Gum	10	20	500	6	Remove
2364	Gum	10	15	300	4	Remove
2365	Paperbark	10	15	300	4	Remove
2366	Gum	10	15	300	4	Remove
2367	Gum	10	15	450	5	Remove
2368	Gum	10	15	450	5	Remove
2369	Gum	10	15	300	4	Remove
2370	Gum	10	15	450	5	Remove
2371	Gum	10	15	450	5	Remove
2372	Gum	15	20	550	7	Remove
2373	Gum	10	15	450	5	Remove
2374	Gum	10	15	350	4	Remove
2375	Gum	10	15	400	5	Remove
2376	Gum	10	15	300	4	Remove

Specimen Details						
Tree ID	Tree Type	Spread (m)	Height (m)	DBH (mm)	TPZ (m)	Retention
2377	Paperbark	10	15	300	4	Remove
2379	Gum	10	15	350	4	Remove
2380	Gum	10	15	350	4	Remove
2381	Gum	10	15	300	4	Remove
2382	Gum	10	15	300	4	Remove
2383	Gum	10	15	350	4	Remove
2384	Gum	10	15	450	5	Remove
2385	Gum	15	20	450	5	Remove
2386	Gum	10	15	300	4	Remove
2387	Gum	10	15	300	4	Remove
2388	Gum	10	15	350	4	Remove
2389	Gum	10	15	350	4	Remove
2390	Gum	10	15	300	4	Remove
2392	Gum	10	15	400	5	Remove
2393	Gum	10	15	300	4	Remove
2394	Gum	10	15	300	4	Remove
2395	Gum	10	15	350	4	Remove
2396	Paperbark	10	15	300	4	Remove
2397	Gum	10	15	300	4	Remove
2398	Gum	10	15	300	4	Remove
2399	Paperbark	10	15	300	4	Remove
2400	Gum	10	15	400	5	Remove
2401	Gum	10	15	350	4	Remove
2402	Paperbark	10	15	350	4	Remove
2403	Gum	10	15	300	4	Remove
2404	Gum	10	15	300	4	Remove
2405	Gum	10	15	300	4	Remove
2407	Gum	10	15	300	4	Remove
2408	Paperbark	10	15	400	5	Remove
2409	Gum	10	15	300	4	Remove

Specimen Details						
Tree ID	Tree Type	Spread (m)	Height (m)	DBH (mm)	TPZ (m)	Retention
2410	Gum	10	15	450	5	Remove
2411	Paperbark	10	15	300	4	Remove
2412	Paperbark	10	15	300	4	Remove
2413	Gum	10	15	400	5	Remove
2414	Gum	10	15	300	4	Remove
2415	Gum	10	15	300	4	Remove
2416	Paperbark	10	15	300	4	Remove
2417	Gum	10	15	400	5	Remove
2418	Gum	10	15	300	4	Remove
2419	Gum	10	15	400	5	Remove
2420	Gum	10	15	300	4	Remove
2426	Gum	10	15	300	4	Remove
2427	Gum	10	15	400	5	Remove
2428	Gum	10	15	400	5	Remove
2429	Gum	10	15	400	5	Remove
2430	Gum	10	15	400	5	Remove
2431	Gum	2	15	400	5	Remove
2432	Gum	15	20	600	7	Remove
2433	Gum	10	15	400	5	Remove
2434	Gum	10	15	400	5	Remove
2435	Gum	10	15	450	5	Remove
2436	Gum	10	15	450	5	Remove
2437	Gum	15	20	500	6	Remove
2438	Gum	10	15	300	4	Remove
2439	Gum	10	15	450	5	Remove
2440	Gum	10	15	300	4	Remove
2441	Gum	10	15	350	4	Remove
2442	Gum	10	15	450	5	Remove
2443	Gum	10	15	350	4	Remove
2444	Gum	15	20	1200	14	Retain

Specimen Details						
Tree ID	Tree Type	Spread (m)	Height (m)	DBH (mm)	TPZ (m)	Retention
2445	Gum	10	15	300	4	Remove
2447	Gum	10	15	400	5	Remove
2448	Gum	10	15	450	5	Remove
2449	Gum	10	15	300	4	Remove
2450	Gum	10	15	300	4	Remove
2451	Gum	10	15	300	4	Remove
2452	Gum	10	15	350	4	Remove
2453	Gum	10	15	300	4	Remove
2456	Gum	10	15	400	5	Remove
2457	Gum	10	15	300	4	Remove
2458	Gum	5	15	350	4	Remove
2459	Gum	10	15	300	4	Remove
2460	Gum	10	15	300	4	Remove
2462	Gum	10	15	300	4	Remove
2463	Gum	10	15	450	5	Remove
2464	Gum	10	15	500	6	Remove
2466	Gum	10	15	300	4	Remove
2468	Gum	10	15	300	4	Remove
2469	Gum	10	15	350	4	Remove
2470	Gum	10	15	400	5	Remove
2471	Gum	10	15	450	5	Remove
2472	Paperbark	10	15	300	4	Remove
2473	Gum	10	15	300	4	Remove
2474	Gum	10	15	300	4	Remove
2475	Gum	10	15	300	4	Remove
2476	Ironbark	4	8	300	4	Retain
2478	Gum	6	13	800	10	Retain
2480	Paperbark	3	5	300	4	Retain
2481	Ironbark	3.5	6	300	4	Retain
2482	Paperbark	4	8	300	4	Retain

Specimen Details						
Tree ID	Tree Type	Spread (m)	Height (m)	DBH (mm)	TPZ (m)	Retention
2483	Ironbark	4	8	300	4	Retain
2484	Gum	5	12	350	4	Retain
2485	Ironbark	3.5	9	300	4	Retain
2486	Ironbark	3.5	9	300	4	Retain
2487	Ironbark	3.5	9	300	4	Retain
2488	Ironbark	6	12	400	5	Retain
2489	Ironbark	4	9	350	4	Retain
2490	Ironbark	4	8	300	4	Retain
2492	Ironbark	8	14	450	5	Retain
2494	Ironbark	5	10	400	5	Retain
2495	Gum	6	15	600	7	Retain
2496	Paperbark	3.5	11	300	4	Retain
2498	Ironbark	3	8	300	4	Retain
2499	Ironbark	4	9	400	5	Retain
2500	Ironbark	4	9	400	5	Retain
2501	Ironbark	4	9	400	5	Retain
2502	Ironbark	3	7	300	4	Retain
2503	Ironbark	3	9	300	4	Retain
2504	Ironbark	3	9	300	4	Retain
2505	Ironbark	3	9	300	4	Retain
2506	Ironbark	4	8	350	4	Retain
2508	Ironbark	4	8	350	4	Retain
2509	Paperbark	4	8	350	4	Retain
2510	Paperbark	3.5	8	300	4	Retain
2511	Ironbark	4	12	350	4	Retain
2512	Ironbark	4	12	350	4	Retain
2513	Ironbark	3	9	300	4	Retain
2514	Ironbark	3	7	300	4	Retain
2515	Paprbark	2.5	7	300	4	Retain
2516	Ironbark	3	7	300	4	Retain

Specimen Details						
Tree ID	Tree Type	Spread (m)	Height (m)	DBH (mm)	TPZ (m)	Retention
2517	Paperbark	3	7	300	4	Retain
2518	Ironbark	3.5	7	300	4	Retain
2521	Ironbark	3	9	300	4	Retain
2523	Ironbark	3	9	300	4	Retain
2524	Ironbark	3	8	300	4	Retain
2525	Ironbark	3	8	300	4	Retain
2526	Ironbark	3	8	300	4	Retain
2527	Ironbark	3	9	300	4	Retain
2529	Ironbark	3	7	300	4	Retain
2530	Ironbark	3	7	300	4	Retain
2531	Gum	8	14	800	10	Retain
2532	Ironbark	3	9	300	4	Retain
2533	Gum	8	14	800	10	Retain
2534	Ironbark	3	9	300	4	Retain
2535	Paperbark	3	10	300	4	Remove
2537	Ironbark	3.5	10	300	4	Remove
2538	Ironbark	3.5	10	300	4	Remove
2539	Ironbark	3.5	10	350	4	Remove
2540	Gum	7	12	600	7	Retain
2541	Gum	7	12	450	5	Retain
2542	Ironbark	4	10	300	4	Retain
2545	Gum	6	12	750	9	Retain
2546	Gum	8	13	800	10	Retain
2547	Gum	6	10	800	10	Retain
2548	Gum	7.5	13	800	10	Retain
2549	Gum	6	10	600	7	Retain
2550	Ironbark	3	10	300	4	Retain
2552	Ironbark	4	8	300	4	Retain
2554	Gum	8	14	900	11	Retain
2556	Ironbark	5	12	300	4	Retain

Specimen Details						
Tree ID	Tree Type	Spread (m)	Height (m)	DBH (mm)	TPZ (m)	Retention
2557	Ironbark	3	8	300	4	Retain
2558	Ironbark	4	9	300	4	Retain
2560	Gum	6	12	800	10	Retain
2562	Ironbark	3	8	300	4	Retain
2563	Gum	6	11	600	7	Retain
2565	Gum	6	12	800	10	Retain
2566	Ironbark	3.5	8	300	4	Retain
2567	Gum	8	11	700	8	Retain
2569	Gum	7.5	12	900	11	Retain
2571	Gum	4.5	9	500	6	Retain
2572	Gum	5	11	600	7	Retain
2573	Gum	8	12	800	10	Retain
2574	Paperbark	4	9	300	4	Retain
2575	Ironbark	3	10	300	4	Retain
2576	Ironbark	3	10	300	4	Retain
2577	Ironbark	3	10	300	4	Retain
2579	Gum	6	10	550	7	Retain
2580	Gum	4	10	400	5	Retain
2581	Gum	5	11	550	7	Retain
2582	Gum	8	13	800	10	Retain
2584	Ironbark	3	7	300	4	Retain
2586	Gum	6	10	750	9	Retain
2587	Gum	5.5	11	800	10	Remove
2588	Ironbark	3.5	9	300	4	Remove
2589	Ironbark	4	11	350	4	Retain
2590	Ironbark	4	11	350	4	Retain
2591	Gum	5	12	500	6	Retain
2592	Gum	9	15	900	11	Retain
2593	Gum	4	10	450	5	Retain
2594	Gum	4	11	400	5	Retain

Specimen Details						
Tree ID	Tree Type	Spread (m)	Height (m)	DBH (mm)	TPZ (m)	Retention
2595	Gum	6	12	700	8	Retain
2596	Ironbark	3.5	9	300	4	Retain
2597	Gum	3.5	11	300	4	Retain
2598	Gum	5	11	400	5	Retain
2599	Ironbark	3	8	300	4	Retain
2600	Ironbark	3	8	300	4	Retain
2601	Ironbark	3	9	300	4	Retain
2602	Gum	6	10	550	7	Retain
2603	Ironbark	3.5	8	300	4	Retain
2604	Gum	4	9	400	5	Retain
2605	Gum	4.5	9	400	5	Retain
2606	Ironbark	5	9	350	4	Retain
2607	Ironbark	6	12	600	7	Retain
2608	Paperbark	5	10	450	5	Retain
2609	Gum	5	11	500	6	Retain
2610	Ironbark	3	8	350	4	Retain
2611	Ironbark	3	9	400	5	Retain
2612	Gum	5.5	10	600	7	Retain
2613	Ironbark	3.5	10	300	4	Retain
2614	Gum	6	11	700	8	Retain
2615	Gum	6	11	450	5	Retain
2616	Gum	6	11	500	6	Retain
2617	Gum	4.5	9	350	4	Retain
2618	Gum	4.5	9	350	4	Retain
2619	Gum	4.5	9	350	4	Retain
2620	Gum	4	10	350	4	Retain
2621	Ironbark	2.5	10	350	4	Retain
2623	Ironbark	5	11	350	4	Retain
2624	Ironbark	5	11	300	4	Retain
2626	Gum	6	10	600	7	Retain

Specimen Details						
Tree ID	Tree Type	Spread (m)	Height (m)	DBH (mm)	TPZ (m)	Retention
2627	Ironbark	3.5	10	350	4	Retain
2628	Ironbark	3.5	10	300	4	Retain
2629	Ironbark	3	10	300	4	Retain
2630	Ironbark	3.5	10	350	4	Retain
2631	Ironbark	4	11	350	4	Retain
2632	Gum	5	12	450	5	Remove
2633	Ironbark	3.5	11	400	5	Retain
2634	Paperbark	3	9	350	4	Retain
2635	Paperbark	3	9	300	4	Retain
2636	Ironbark	4	10	300	4	Retain
2637	Ironbark	3.5	10	300	4	Retain
2638	Gum	4	10	450	5	Retain
2639	Gum	5.5	11	450	5	Retain
2640	Gum	6	12	400	5	Remove
2641	Gum	6.5	12	400	5	Remove
2642	Paperbark	3.5	8	300	4	Remove
2643	Paperbark	3.5	10	300	4	Remove
2644	Ironbark	5	10	350	4	Remove
2645	Ironbark	4	9	300	4	Remove
2647	Ironbark	3.5	9	300	4	Remove
2648	Ironbark	3.5	10	350	4	Remove
2650	Ironbark	3	9	300	4	Remove
2651	Gum	5	9	300	4	Remove
2653	Gum	4	8	300	4	Remove
2654	Gum	3.5	12	800	10	Remove
2655	Gum	3	10	300	4	Remove
2656	Gum	8	10	400	5	Remove
2657	Ironbark	3	10	300	4	Retain
2658	Gum	6	11	350	4	Retain
2660	Paperbark	2	8	300	4	Remove

Specimen Details						
Tree ID	Tree Type	Spread (m)	Height (m)	DBH (mm)	TPZ (m)	Retention
2661	Paperbark	2	8	300	4	Remove
2662	Paperbark	2	10	300	4	Remove
2664	Ironbark	5	11	350	4	Retain
2665	Ironbark	3	9	300	4	Remove
2666	Ironbark	0.5	9	300	4	Remove
2668	Ironbark	2.5	8	300	4	Remove
2669	Ironbark	2	8	300	4	Retain
2670	Ironbark	3.5	10	300	4	Retain
2671	Ironbark	4	11	300	4	Retain
2672	Ironbark	4	9	300	4	Remove
2673	Ironbark	3	8	300	4	Remove
2674	Ironbark	4	9	300	4	Remove
2675	Ironbark	5	11	350	4	Remove
2676	Ironbark	3	9	300	4	Remove
2677	Ironbark	5	10	300	4	Remove
2678	Ironbark	3	10	300	4	Remove
2679	Ironbark	3.5	9	300	4	Remove
2680	Gum	8	12	800	10	Retain
2681	Gum	6	10	600	7	Remove
2683	Gum	7	10	500	6	Remove
2684	Ironbark	5	9	300	4	Remove
2685	Gum	6	10	450	5	Remove
2686	Ironbark	3	8	300	4	Remove
2687	Paperbark	2	9	300	4	Remove
2688	Paperbark	3	9	300	4	Remove
2689	Gum	4	10	300	4	Remove
2690	Ironbark	5	11	350	4	Remove
2691	Gum	7	10	350	4	Remove
2692	Ironbark	4	10	300	4	Remove
2694	Gum	5	11	550	7	Remove

Specimen Details						
Tree ID	Tree Type	Spread (m)	Height (m)	DBH (mm)	TPZ (m)	Retention
2695	Paperbark	2.5	8	300	4	Remove
2696	Ironbark	4	9	400	5	Remove
2697	Ironbark	3	9	300	4	Remove
2698	Ironbark	3	9	300	4	Remove
2699	Ironbark	4	9	300	4	Remove
2700	Gum	7	11	500	6	Remove
2701	Ironbark	3.5	9	300	4	Remove
2702	Gum	5	10	500	6	Remove
2703	Ironbark	3	7	300	4	Remove
2704	Gum	4	9	400	5	Remove
2705	Gum	8	11	600	7	Remove
2707	Paperbark	3	7	300	4	Remove
2709	Paperbark	2	8	300	4	Remove
2711	Ironbark	5	10	400	5	Remove
2712	Ironbark	3.5	10	400	5	Remove
2713	Gum	6	11	600	7	Remove
2714	Paperbark	4	9	300	4	Remove
2715	Gum	5	10	400	5	Remove
2716	Ironbark	3	10	300	4	Remove
2717	Ironbark	3	8	300	4	Remove
2718	Ironbark	2.5	8	300	4	Remove
2720	Gum	5	9	400	5	Remove
2721	Ironbark	4	7	300	4	Remove
2722	Ironbark	4	9	300	4	Remove
2724	Ironbark	4	8	300	4	Remove
2725	Ironbark	3	9	300	4	Remove
2726	Ironbark	3	9	300	4	Remove
2727	Gum	6	11	300	4	Remove
2728	Ironbark	3.5	10	300	4	Remove
2729	Ironbark	3.5	10	300	4	Remove

Specimen Details						
Tree ID	Tree Type	Spread (m)	Height (m)	DBH (mm)	TPZ (m)	Retention
2730	Gum	6	12	450	5	Remove
2731	Ironbark	3.5	10	300	4	Remove
2732	Ironbark	3.5	9	300	4	Remove
2734	Ironbark	4	10	300	4	Remove
2735	Ironbark	3	10	300	4	Remove
2736	Ironbark	3	10	300	4	Remove
2737	Ironbark	4	10	350	4	Remove
2738	Ironbark	3	12	300	4	Remove
2739	Ironbark	4	10	300	4	Remove
2740	Paperbark	3.5	10	300	4	Remove
2742	Paperbark	2.5	10	350	4	Remove
2743	Paperbark	2.5	10	300	4	Remove
2744	Ironbark	3	9	300	4	Remove
2745	Paperbark	4	9	350	4	Remove
2746	Paperbark	3	8	300	4	Remove
2747	Ironbark	3.5	7	300	4	Remove
2748	Gum	7	13	800	10	Remove
2749	Gum	5	10	400	5	Remove
2750	Gum	5	10	450	5	Remove
2751	Gum	7	11	600	7	Remove
2753	Ironbark	4	10	350	4	Remove
2754	Paperbark	3	9	300	4	Remove
2755	Ironbark	1.5	9	300	4	Remove
2756	Ironbark	3	10	300	4	Remove
2757	Ironbark	3.5	10	300	4	Remove
2758	Ironbark	2.5	10	400	5	Remove
2759	Ironbark	4	9	300	4	Remove
2760	Ironbark	3.5	11	300	4	Remove
2761	Ironbark	3.5	11	300	4	Remove
2762	Ironbark	3.5	11	300	4	Remove

Specimen Details						
Tree ID	Tree Type	Spread (m)	Height (m)	DBH (mm)	TPZ (m)	Retention
2763	Gum	8	13	850	10	Remove
2765	Gum	5	20	300	4	Retain
2766	Gum	5	20	300	4	Retain
2768	Gum	10	30	600	7	Retain
2769	Gum	15	30	600	7	Retain
2771	Gum	10	25	400	5	Retain
2772	Gum	5	15	300	4	Retain
2773	Gum	5	20	300	4	Retain
2774	Gum	5	15	300	4	Retain
2775	Gum	10	20	400	5	Retain
2776	Gum	10	20	400	5	Retain
2777	Gum	10	20	500	6	Retain
2778	Gum	5	15	400	5	Retain
2779	Gum	5	15	300	4	Retain
2780	Gum	5	15	300	4	Retain
2782	Gum	10	25	500	6	Retain
2784	Gum	15	25	700	8	Retain
2785	Gum	10	25	400	5	Retain
2786	Gum	5	15	300	4	Retain
2787	Gum	10	25	500	6	Retain
2788	Gum	10	20	400	5	Retain
2789	Gum	10	20	400	5	Retain
2790	Gum	10	30	600	7	Retain
2791	Gum	15	30	700	8	Retain
2792	Gum	15	30	700	8	Retain
2793	Gum	5	15	300	4	Retain
2794	Gum	15	30	600	7	Retain
2795	Gum	5	15	300	4	Retain
2796	Gum	5	15	300	4	Retain
2798	Gum	10	20	400	5	Retain

Specimen Details						
Tree ID	Tree Type	Spread (m)	Height (m)	DBH (mm)	TPZ (m)	Retention
2799	Gum	15	30	500	6	Retain
2801	Gum	10	20	400	5	Retain
2802	Gum	10	30	600	7	Retain
2803	Gum	5	15	400	5	Retain
2804	Gum	5	15	400	5	Retain
2805	Gum	15	30	500	6	Retain
2806	Gum	15	30	600	7	Retain
2807	Gum	15	30	600	7	Retain
2808	Gum	5	20	500	6	Retain
2809	Gum	5	20	500	6	Retain
2811	Gum	10	25	400	5	Retain
2812	Gum	10	25	400	5	Retain
2813	Gum	5	15	300	4	Retain
2816	Gum	10	25	400	5	Retain
2817	Gum	5	20	300	4	Retain
2818	Gum	10	20	500	6	Retain
2819	Gum	5	15	300	4	Retain
2820	Gum	5	15	300	4	Retain
2821	Gum	10	25	500	6	Retain
2822	Gum	5	20	300	4	Retain
2823	Gum	15	30	600	7	Retain
2824	Gum	5	15	300	4	Retain
2826	Gum	10	20	400	5	Retain
2827	Gum	10	25	500	6	Retain
2828	Gum	5	20	400	5	Retain
2829	Gum	10	25	500	6	Retain
2830	Gum	15	30	600	7	Retain
2831	Gum	10	30	500	6	Retain
2832	Gum	5	20	300	4	Retain
2833	Gum	15	30	700	8	Retain

Specimen Details						
Tree ID	Tree Type	Spread (m)	Height (m)	DBH (mm)	TPZ (m)	Retention
2834	Gum	15	30	500	6	Retain
2835	Gum	15	30	500	6	Retain
2838	Gum	10	25	400	5	Retain
2839	Gum	10	25	400	5	Retain
2840	Gum	10	25	400	5	Retain
2841	Gum	10	25	400	5	Retain
2842	Gum	5	20	300	4	Retain
2843	Gum	5	20	300	4	Retain
2844	Gum	5	20	300	4	Retain
2845	Gum	5	20	300	4	Retain
2846	Gum	5	20	300	4	Retain
2847	Gum	5	20	300	4	Retain
2848	Gum	5	20	300	4	Retain
2849	Gum	5	20	400	5	Retain
2850	Gum	5	15	300	4	Retain
2851	Gum	10	20	500	6	Retain
2852	Gum	5	20	400	5	Retain
2853	Gum	5	15	300	4	Retain
2854	Gum	10	30	600	7	Retain
2855	Gum	5	15	300	4	Retain
2856	Gum	15	30	700	8	Retain
2857	Native	5	15	300	4	Retain
2858	Gum	5	15	300	4	Retain
2859	Gum	5	20	400	5	Retain
2860	Gum	10	25	400	5	Retain
2861	Gum	10	20	400	5	Retain
2862	Gum	5	15	300	4	Retain
2863	Gum	5	20	400	5	Retain
2864	Gum	10	20	400	5	Retain
2865	Gum	5	15	300	4	Retain

Specimen Details						
Tree ID	Tree Type	Spread (m)	Height (m)	DBH (mm)	TPZ (m)	Retention
2866	Gum	5	20	400	5	Retain
2867	Gum	10	20	400	5	Retain
2868	Gum	5	20	400	5	Retain
2869	Gum	5	15	300	4	Retain
2870	Gum	5	20	300	4	Retain
2871	Gum	5	20	400	5	Retain
2873	Gum	5	15	300	4	Retain
2874	Gum	5	20	400	5	Retain
2875	Gum	5	20	400	5	Retain
2876	Gum	10	20	400	5	Retain
2877	Gum	10	20	400	5	Retain
2878	Gum	5	15	300	4	Retain
2879	Gum	5	15	300	4	Retain
2880	Gum	15	30	600	7	Retain
2881	Gum	5	20	400	5	Retain
2882	Gum	10	25	500	6	Retain
2883	Gum	10	25	400	5	Retain
2885	Gum	5	15	300	4	Retain
2886	Gum	10	25	500	6	Retain
2887	Gum	15	30	600	7	Retain
2889	Gum	5	20	400	5	Retain
2890	Gum	10	20	400	5	Remove
2892	Gum	5	15	300	4	Retain
2893	Gum	10	25	500	6	Retain
2894	Gum	5	15	300	4	Retain
2895	Gum	5	15	300	4	Retain
2897	Gum	5	20	300	4	Retain
2898	Gum	5	20	400	5	Retain
2899	Gum	10	30	600	7	Retain
2900	Gum	10	25	400	5	Retain

Specimen Details						
Tree ID	Tree Type	Spread (m)	Height (m)	DBH (mm)	TPZ (m)	Retention
2901	Gum	10	25	500	6	Remove
2903	Gum	15	30	600	7	Remove
2904	Gum	15	30	500	6	Remove
2905	Gum	10	20	500	6	Remove
2906	Gum	5	20	300	4	Remove
2907	Gum	10	25	500	6	Retain
2909	Gum	5	15	300	4	Retain
2912	Gum	5	15	300	4	Remove
2913	Gum	5	15	400	5	Remove
2915	Gum	10	25	450	5	Remove
2916	Gum	5	15	400	5	Retain
2917	Gum	5	15	300	4	Retain
2918	Gum	5	15	300	4	Retain
2919	Gum	5	20	400	5	Retain
2920	Gum	10	25	450	5	Retain
2921	Gum	5	15	300	4	Retain
2922	Gum	10	30	600	7	Retain
2923	Gum	10	25	450	5	Retain
2924	Gum	10	20	400	5	Retain
2925	Gum	5	15	400	5	Retain
2926	Gum	15	30	800	10	Retain
2927	Gum	10	25	400	5	Retain
2928	Gum	10	25	400	5	Retain
2929	Gum	10	20	400	5	Retain
2930	Gum	10	20	400	5	Retain
2931	Gum	5	20	300	4	Retain
2932	Gum	10	25	500	6	Retain
2933	Gum	10	25	500	6	Retain
2934	Gum	10	20	400	5	Retain
2935	Gum	10	20	400	5	Retain

Specimen Details						
Tree ID	Tree Type	Spread (m)	Height (m)	DBH (mm)	TPZ (m)	Retention
2936	Gum	15	30	700	8	Retain
2937	Gum	5	15	300	4	Retain
2938	Gum	10	20	400	5	Retain
2939	Gum	10	25	800	10	Retain
2940	Gum	5	20	400	5	Retain
2941	Gum	5	15	400	5	Retain
2943	Gum	5	15	300	4	Retain
2944	Gum	10	25	450	5	Retain
2947	Gum	5	15	300	4	Retain
2948	Gum	10	30	500	6	Retain
2949	Gum	5	20	400	5	Retain
2951	Gum	5	15	300	4	Retain
2952	Gum	10	20	400	5	Retain
2954	Gum	5	20	300	4	Retain
2955	Gum	10	20	300	4	Retain
2956	Gum	15	30	600	7	Retain
2957	Gum	5	10	300	4	Retain
2958	Gum	5	20	400	5	Retain
2959	Gum	15	25	600	7	Retain
2960	Gum	5	15	300	4	Retain
2961	Gum	5	15	300	4	Retain
2962	Gum	5	15	300	4	Retain
2963	Gum	5	15	300	4	Retain
2964	Gum	5	15	300	4	Retain
2965	Gum	10	20	400	5	Remove
2966	Gum	10	30	500	6	Remove
2967	Paperbark	5	15	300	4	Remove
2968	Gum	5	20	400	5	Remove
2969	Gum	10	25	500	6	Remove
2970	Gum	15	30	600	7	Remove

Specimen Details						
Tree ID	Tree Type	Spread (m)	Height (m)	DBH (mm)	TPZ (m)	Retention
2971	Gum	10	15	300	4	Remove
2972	Gum	10	25	500	6	Remove
2973	Gum	15	30	600	7	Remove
2975	Gum	15	30	600	7	Remove
2976	Gum	10	25	400	5	Remove
2978	Gum	10	25	400	5	Remove
2979	Paperbark	5	15	300	4	Remove
2980	Gum	10	20	400	5	Remove
2981	Gum	5	20	400	5	Remove
2982	Gum	10	25	500	6	Remove
2983	Paperbark	5	15	300	4	Remove
2984	Gum	10	30	600	7	Retain
2985	Gum	10	25	500	6	Retain
2986	Gum	10	30	500	6	Retain
2987	Gum	5	15	300	4	Retain
2988	Gum	15	30	700	8	Retain
2989	Gum	5	10	300	4	Retain
2990	Gum	10	20	400	5	Retain
2991	Gum	15	30	700	8	Retain
2992	Gum	5	15	300	4	Retain
2993	Gum	5	15	300	4	Retain
2994	Gum	15	30	700	8	Retain
2995	Gum	10	20	400	5	Retain
2996	Gum	10	20	400	5	Retain
2997	Gum	5	15	300	4	Retain
2998	Gum	5	20	400	5	Retain
2999	Gum	15	20	400	5	Retain
3000	Gum	10	20	400	5	Retain
3001	Gum	10	20	400	5	Retain
3002	Gum	5	15	300	4	Retain

Specimen Details						
Tree ID	Tree Type	Spread (m)	Height (m)	DBH (mm)	TPZ (m)	Retention
3003	Gum	10	20	500	6	Retain
3004	Gum	10	25	400	5	Retain
3005	Gum	5	10	400	5	Retain
3006	Gum	15	20	400	5	Retain
3007	Gum	10	20	400	5	Retain
3008	Gum	5	15	300	4	Retain
3009	Gum	5	15	300	4	Retain
3011	Gum	10	25	500	6	Retain
3012	Gum	5	15	400	5	Retain
3013	Gum	15	30	600	7	Remove
3014	Gum	15	30	600	7	Remove
3015	Gum	10	25	450	5	Remove
3016	Gum	5	15	300	4	Remove
3017	Gum	5	15	300	4	Retain
3018	Paperbark	5	15	300	4	Retain
3019	Paperbark	5	15	300	4	Remove
3020	Paperbark	5	15	300	4	Remove
3021	Paperbark	5	15	300	4	Remove
3022	Gum	15	30	700	8	Remove
3023	Paperkark	5	15	300	4	Remove
3024	Gum	10	25	500	6	Remove
3025	Gum	5	15	300	4	Remove
3026	Gum	5	15	300	4	Remove
3028	Gum	5	15	300	4	Remove
3029	Gum	10	30	700	8	Remove
3030	Gum	5	15	300	4	Remove
3031	Gum	5	20	300	4	Remove
3032	Gum	5	20	300	4	Remove
3033	Paperbark	5	15	300	4	Remove
3034	Paperbark	5	15	300	4	Remove

Specimen Details						
Tree ID	Tree Type	Spread (m)	Height (m)	DBH (mm)	TPZ (m)	Retention
3035	Gum	10	25	400	5	Remove
3036	Gum	5	20	300	4	Remove
3037	Gum	5	15	300	4	Remove
3038	Gum	10	25	400	5	Remove
3039	Paperbark	10	20	700	8	Remove
3040	Paperbark	5	15	300	4	Remove
3041	Paperbark	5	15	300	4	Remove
3042	Paperbark	5	15	300	4	Remove
3043	Gum	15	30	600	7	Remove
3044	Gum	10	20	400	5	Remove
3045	Gum	10	20	400	5	Remove
3046	Gum	10	20	400	5	Remove
3047	Gum	10	25	400	5	Remove
3048	Gum	5	20	300	4	Remove
3049	Gum	5	20	300	4	Remove
3050	Gum	10	25	400	5	Remove
3051	Gum	10	20	400	5	Remove
3052	Gum	10	20	300	4	Retain
3053	Gum	10	20	300	4	Retain
3054	Gum	5	15	300	4	Retain
3055	Gum	5	20	400	5	Retain
3056	Gum	5	20	400	5	Retain
3058	Gum	15	25	500	6	Retain
3059	Paperbark	5	20	400	5	Retain
3060	Gum	15	30	600	7	Retain
3061	Gum	5	15	300	4	Retain
3062	Gum	5	15	300	4	Retain
3063	Gum	5	15	300	4	Retain
3064	Gum	5	20	400	5	Retain
3065	Gum	5	15	300	4	Retain

Specimen Details						
Tree ID	Tree Type	Spread (m)	Height (m)	DBH (mm)	TPZ (m)	Retention
3066	Gum	15	30	700	8	Retain
3067	Gum	5	15	300	4	Retain
3068	Gum	5	15	300	4	Retain
3069	Gum	5	15	300	4	Retain
3070	Gum	10	20	400	5	Retain
3071	Gum	5	15	300	4	Retain
3072	Gum	5	20	400	5	Retain
3073	Gum	5	20	400	5	Retain
3074	Gum	10	20	500	6	Retain
3075	Gum	5	15	400	5	Remove
3076	Gum	5	20	400	5	Remove
3077	Gum	5	15	300	4	Retain
3078	Gum	5	15	400	5	Retain
3079	Gum	10	20	400	5	Remove
3080	Gum	5	15	300	4	Remove
3081	Gum	10	25	500	6	Remove
3083	Gum	5	15	300	4	Remove
3084	Gum	5	15	300	4	Remove
3085	Gum	5	15	300	4	Remove
3086	Gum	5	15	300	4	Remove
3087	Gum	5	15	300	4	Remove
3088	Gum	10	25	500	6	Remove
3089	Gum	10	25	400	5	Remove
3090	Gum	10	25	500	6	Remove
3091	Gum	10	25	400	5	Remove
3092	Gum	10	20	300	4	Remove
3093	Gum	10	20	400	5	Remove
3094	Gum	15	25	500	6	Remove
3095	Gum	10	20	300	4	Remove
3096	Paperbark	10	20	400	5	Remove

Specimen Details						
Tree ID	Tree Type	Spread (m)	Height (m)	DBH (mm)	TPZ (m)	Retention
3097	Gum	5	15	300	4	Remove
3098	Paperbark	5	15	300	4	Remove
3100	Paperbark	5	15	300	4	Remove
3101	Gum	10	25	600	7	Remove
3102	Gum	15	25	600	7	Remove
3104	Paperbark	5	15	300	4	Remove
3105	Gum	15	25	600	7	Remove
3106	Gum	15	25	600	7	Remove
3107	Gum	10	25	400	5	Remove
3108	Paperbark	5	15	300	4	Remove
3109	Gum	10	25	400	5	Remove
3110	Paperbark	5	15	300	4	Remove
3111	Paperbark	5	15	300	4	Remove
3112	Gum	10	30	500	6	Remove
3113	Paperbark	5	15	300	4	Remove
3114	Gum	10	20	400	5	Remove
3115	Gum	5	15	300	4	Remove
3116	Gum	15	30	500	6	Remove
3117	Gum	10	25	600	7	Remove
3118	Gum	10	25	500	6	Remove
3119	Gum	10	20	400	5	Remove
3120	Gum	10	20	400	5	Remove
3121	Gum	5	15	300	4	Remove
3122	Gum	5	15	300	4	Remove
3124	Gum	10	25	500	6	Remove
3125	Paperbark	5	15	300	4	Remove
3126	Paperbark	10	20	400	5	Remove
3127	Gum	5	15	300	4	Remove
3128	Gum	10	25	400	5	Remove
3129	Gum	5	20	300	4	Remove

Specimen Details						
Tree ID	Tree Type	Spread (m)	Height (m)	DBH (mm)	TPZ (m)	Retention
3130	Gum	5	20	300	4	Remove
3131	Gum	5	20	400	5	Remove
3132	Paperbark	5	15	300	4	Remove
3133	Paperbark	5	15	300	4	Remove
3134	Paperbark	5	15	400	5	Remove
3135	Paperbark	5	15	300	4	Remove
3136	Paperbark	5	15	400	5	Remove
3137	Paperbark	5	15	300	4	Remove
3138	Paperbark	5	15	300	4	Remove
3139	Gum	15	30	800	10	Remove
3140	Gum	10	25	400	5	Remove
3141	Gum	10	25	400	5	Remove
3142	Gum	15	25	700	8	Remove
3143	Gum	15	25	500	6	Remove
3144	Gum	5	15	300	4	Remove
3145	Gum	10	25	500	6	Remove
3146	Gum	10	25	400	5	Remove
3147	Gum	5	15	300	4	Remove
3148	Gum	5	15	300	4	Remove
3149	Gum	15	30	600	7	Remove
3150	Gum	10	20	400	5	Remove
3151	Gum	15	25	600	7	Remove
3152	Gum	5	15	400	5	Remove
3153	Gum	5	15	400	5	Remove
3154	Gum	10	25	400	5	Remove
3155	Paperbark	5	15	300	4	Remove
3156	Gum	10	20	400	5	Remove
3157	Gum	10	20	400	5	Remove
3158	Gum	10	25	500	6	Remove
3159	Gum	15	25	600	7	Remove

Specimen Details						
Tree ID	Tree Type	Spread (m)	Height (m)	DBH (mm)	TPZ (m)	Retention
3160	Gum	10	20	400	5	Remove
3162	Paperbark	5	15	300	4	Remove
3163	Paperbark	5	15	300	4	Remove
3164	Paperbark	10	20	400	5	Remove
3165	Gum	10	25	300	4	Remove
3166	Gum	5	20	400	5	Remove
3167	Gum	10	20	500	6	Remove
3168	Gum	15	30	600	7	Remove
3169	Gum	10	25	400	5	Remove
3170	Gum	5	15	300	4	Remove
3171	Gum	10	25	400	5	Remove
3172	Gum	10	20	400	5	Remove
3173	Paperbark	5	20	400	5	Remove
3174	Gum	10	25	500	6	Remove
3175	Gum	15	25	500	6	Remove
3176	Paperbark	5	15	300	4	Remove
3177	Gum	10	20	500	6	Remove
3178	Paperbark	5	15	400	5	Remove
3179	Paperbark	5	15	300	4	Remove
3180	Gum	5	20	400	5	Remove
3181	Paperbark	5	15	400	5	Remove
3182	Paperbark	5	15	300	4	Remove
3183	Gum	10	25	500	6	Remove
3186	Gum	5	15	300	4	Remove
3187	Gum	5	15	400	5	Remove
3189	Gum	15	25	500	6	Remove
3190	Gum	5	20	400	5	Remove
3191	Gum	5	15	300	4	Remove
3192	Gum	5	15	300	4	Remove
3194	Gum	10	20	500	6	Remove

Specimen Details						
Tree ID	Tree Type	Spread (m)	Height (m)	DBH (mm)	TPZ (m)	Retention
3195	Gum	5	20	300	4	Remove
3196	Gum	5	20	400	5	Remove
3197	Gum	5	15	800	10	Remove
3198	Gum	5	15	400	5	Remove
3199	Gum	5	20	300	4	Remove
3200	Gum	5	20	300	4	Remove
3201	Gum	10	20	400	5	Remove
3202	Gum	5	15	300	4	Remove
3203	Paperbark	5	15	400	5	Remove
3204	Gum	10	30	500	6	Remove
3205	Gum	5	20	300	4	Remove
3206	Gum	5	20	300	4	Remove
3207	Gum	5	20	300	4	Remove
3208	Gum	10	20	400	5	Remove
3209	Gum	5	15	300	4	Remove
3210	Gum	5	20	400	5	Remove
3211	Gum	5	20	400	5	Remove
3212	Gum	5	15	300	4	Remove
3213	Gum	10	20	300	4	Remove
3214	Gum	5	20	400	5	Remove
